



SANTA ROSA COUNTY PROCUREMENT DEPARTMENT

6495 Caroline Street, Suite J | Milton, Florida 32570

DAVID KING
davidk@santarosa.fl.gov

BID OPENING October 11, 2016

**Santa Rosa County Procurement Conference Room
Milton, Florida**

Present: For Santa Rosa County:

Dave King - Procurement Officer; Glenn Bailey – Assistant Public Works
Director

Others in attendance:

Tony McKnight – Pensacola Concrete Construction; Gene Williams – Main Street
Construction; Craig Helms – Site & Utility; Michael Taylor – McDelt; Mitt
Fulmer – Floridian Construction; Jill Radford, Tyler Clukey – Gulf Atlantic;
Ryan – David Taylor Construction

The meeting opened at 10:00 a.m.

The purpose of the meeting was to receive bids for the Ortega Street Sidewalk Project.

The following were received:

Ortega Street Sidewalk

BID# 2016-061:

1. Gulf Coast Industrial Construction, LLC	\$46,546.50
2. Site and Utility, LLC	\$62,180.00
3. Floridian Construction & Development Co., Inc.	\$67,846.00
4. Main Street Construction Services, LLC	\$74,899.00
5. Pensacola Concrete Construction Co., Inc.	\$79,937.50
6. LAS Contracting Corp	\$88,953.00
7. McDelt, LLC	\$99,258.00
8. Dominguez Design-Build, Inc.	\$101,700.00
9. Gulf Atlantic Constructors, Inc.	\$154,050.00
10. David Taylor Construction	Rejected-Late Delivery

**INVITATION TO BID
ORTEGA STREET SIDEWALKS**

Notice is hereby given that the Board of County Commissioners of Santa Rosa County, Florida will receive sealed bids for construction and installation of concrete sidewalks located on Ortega Street, Navarre, FL. Only properly licensed and insured contractors are invited to submit proposals.

All bids must be in writing and delivered by hand, overnight courier service, or U.S. Mail to the Santa Rosa County Procurement Department, 6495 Caroline Street, Suite J, Milton, Florida 32570, and must be received by 10:00 a.m., October 11, 2016, at which time will be publicly opened. Secondary delivery location shall be to Suite M at the above address. Only bids received by the aforesaid time and date will be considered. All bids shall be sealed and clearly labeled, "**ITB 16-061 ORTEGA STREET SIDEWALK**". Please provide the original proposal, labeled "ORIGINAL", and FOUR (4) copies labeled "COPY" (5 total complete packages) along with one (1) electronic file in OCR (readable) PDF format.

A Pre-Bid conference will be held 10.00 a.m., October 3, 2016 at the intersection of Ortega Street and Laredo Street in Navarre, Florida. All interested parties are invited to attend. It is strongly recommended those interested in submitting bids attend.

Specifications may be secured by download from the Santa Rosa County Website:
www.santarosa.fl.gov (Bids).

Questions concerning this bid should be directed to Glenn Bailey at glennb@santarosa.fl.gov prior to 4:30 p.m., October 7, 2016.

Each bid shall be submitted on the bid form provided and must be accompanied by a Certified Check or bid Bond in the amount of five percent (5%) of the Base Bid as Bid Security, and copies of all required licenses. Such Bid Bond or Check is given with the understanding and agreement that it guarantees: (1) that the bidder will not withdraw his bid for a period of 60 days after the bids have been opened; and, (2) that if his bid is accepted, the Bidder will enter into the written Contract with Santa Rosa County and furnish the required Performance Bond Payment Bond Insurance Certificates, within 10 days after receipt of Notice of Award of his bid. Pursuant to Florida Statutes, Section 255.05, should the contract exceed \$100,000, the Contractor shall be required to execute and record performance and payment bonds. These bonds must state the name and principal business address of both the principal and the surety and a description of the project sufficient to identify it. In the event the bidder fails to comply with any of these conditions and requirements in whole or in part, the full amount of the bond or check shall be automatically forfeited to Santa Rosa County as damages on account of the default of the bidder. Otherwise, Certified Checks shall be returned to bidders in accordance with Procurement Procedures and bid Bonds shall be let to expire unless return is requested by the submitter.

The Board of County Commissioners reserves the right to accept or reject any and all bids in whole or in part and to waive all informalities and to award the bid that it determines to be in the best interest of Santa Rosa County. Santa Rosa County does not discriminate on the basis of race, color, national origin, sex, religion, age, or handicapped status in employment or provision of service.

By order of the Board of County Commissioners of Santa Rosa County, Florida

PROJECT MANUAL
FOR
ORTEGA STREET SIDEWALK PROJECT



SANTA ROSA COUNTY FLORIDA

DISTRICT ONE	VACANT
DISTRICT TWO	ROBERT "BOB" COLE
DISTRICT THREE	W.D. "DON" SALTER
DISTRICT FOUR	ROB WILLIAMSON
DISTRICT FIVE	LANE LYNCHARD, CHAIRMAN

September
2016

CONTENTS

Invitation to Bid	5
Scope of Work	6
Instruction to Bidders	9
Proposal/Bid Form	11
Insurance Requirements.....	13
General Provisions	15
Sworn Statement on Public Entity Crimes	48

INVITATION TO BID
ORTEGA STREET SIDEWALK PROJECT

Only properly licensed contractors are invited to bid on the Ortega Street Sidewalk Project. This work includes the installation/construction of concrete sidewalks as shown in attached aerial map/plan.

The Board of County Commissioners of Santa Rosa County, Florida (Owner) will receive sealed bids from qualified licensed contractors only until 10:00 A.M. (CST), October 11, 2016; at the Santa Rosa County Procurement Department, 6495 Caroline Street Suite J, Milton, Florida 32570. Bids received after this time will be rejected and returned unopened to the bidder. Bids will be opened publicly and read aloud. All interested parties are invited to attend.

Bid documents, Scope of Work, including single line diagram/map, sketch and specifications relative thereto may be inspected at the Santa Rosa County Procurement Department, 6495 Caroline Street, Suite J, Milton, Florida. Bid documents, Scope of Work, including single line diagram/map, sketch and specification may be secured from the Santa Rosa County Procurement website: www.santarosa.fl.gov (Bids).

A pre-bid meeting will be held on October 3, 2016 at 10:00 A.M., on site at the intersection of Ortega Street and Laredo Street Navarre, FL; attendance is strongly recommended. All interested parties are invited to attend.

Questions concerning this project should be directed, in writing, to Glenn Bailey at glennb@santarosa.fl.gov prior to October 7, 2016 at 4:30 P. M.

The project will be awarded to the lowest responsive and responsible bidder meeting all qualifications set forth in the project manual.

Each bid shall be submitted on the bid form shown and must be accompanied by a Certified Check or Bid Bond in the amount of five percent (5%) of the Base Bid, and copies of appropriate licenses. Such Bid Bond or Check is given with the understanding and agreement that it guarantees: (1) that the bidder will not withdraw his bid for a period of 60 days after the bids have been opened; and, (2) that if his bid is accepted, the Bidder will enter into the written Contract with Santa Rosa County and furnish the required Performance Bond Payment Bond Insurance Certificates, within 10 days after receipt of Notice of Award of his bid. Pursuant to Florida Statutes, Section 255.05, should the contract exceed \$100,000, the Contractor shall be required to execute and record the performance and payment bonds. The bonds must state the name and principal business address of both the principal and the surety and a description of the project sufficient to identify it. In the event the bidder fails to comply with any of these conditions and requirements in whole or in part, the full amount of the bond or check shall be automatically forfeited to Santa Rosa County as damages on account of the default of the bidder.

The Owner reserves the right to waive informalities in bids, to reject any or all bids with or without cause and to accept the bid that in its judgment is in the best interest of Santa Rosa County, Florida.

The Contract form shall be provided by the County Attorney.

Completion Time: The entire project shall be completed within ninety (90) calendar days after the Notice to Proceed.

The date of substantial completion of the work or designated portion thereof is the date certified by the Engineer when construction is sufficiently complete and approved in accordance with the Contract Documents so the Owner can occupy or utilize the work for the use which it was intended.

Liquidated damages will be established in the amount of \$500.00 per calendar day for each calendar day after completion date if the work is not substantially complete as certified by the Engineer.

Payment requests approved by the Engineer for work completed satisfactorily in accordance with the Contract Documents shall be reduced by a ten percent (10%) retainer. The ten percent (10%) retainer shall be retained by the Owner until final completion and acceptance of the work by the Engineer.

Santa Rosa County Board of County Commissioners encourages all segments of the business community to participate in its procurement opportunities, including small businesses, minority/women owned businesses, and disadvantaged business enterprises. The Board does not discriminate on the basis of race, color, religion, national origin, disability, sex, or age in the administration of contracts.

SCOPE OF WORK

The scope of work is to construct concrete sidewalks on Ortega Street from Branston Street south to Navarre Parkway. (See attached map and cross section below). The single line diagram/map below indicates general sidewalk location. Exact sidewalk alignment shall be coordinated with county Public Works Department prior to construction. The sidewalk shall be constructed to match the existing grade. The sidewalk will have a transverse slope either toward or away from the road to maintain existing drainage patterns. Minor cut and fill will be required during construction to provide a smooth transition of the sidewalk and maintain existing drainage patterns.

Work shall include the following:

- 1) Prepare site for concrete sidewalk. Scarify soil, remove top soil/organics/vegetation and compact native soil. Remove unsuitable soils, replace with granular fill, and compact. Santa Rosa County shall provide and deliver suitable fill as required. Fill material will be stock piled within the project area. Fill material shall be placed and compacted by contractor.
- 2) Form, place and finish two (2) sections of new concrete sidewalks as shown in attached site plan. Section A sidewalk from Branston Street (just south of Branston at the end of existing sidewalk) to Olivera Street shall be 4" thick, 5' wide and approximately 1075 LF. Section B sidewalk from Olivera Street to Navarre Parkway shall be 4" thick, 5' wide and approximately 1313 LF. The project is divided into the two sidewalk sections A and B for the purpose of scheduling and possible phasing depending on funds availability. Please provide a quote for each section of sidewalk as well as a total (Base Bid) using the bid table below.
- 3) Sidewalk finish shall match existing adjacent sidewalks on Ortega Street.
- 4) Sidewalks shall have a minimum strength of 2500 pounds per square inch (PSI) and be reinforced with woven wire fabric or fiber reinforced concrete.
- 5) Sidewalks shall be constructed with a maximum of ¼ inch in 12 inches slope.
- 6) Sidewalks shall conform to ADA requirements.
- 7) Sidewalks shall have ADA ramps with detectible warnings at all street intersections.
- 8) One-half (1/2) inch expansion joints shall be at thirty (30) foot intervals or less, with control joints at ten (10) foot intervals.
- 9) Contractor shall be responsible for any incidental work associated with sidewalk construction such as utility valve box adjustments, irrigation repairs/relocates etc.
- 10) Contractor shall remove and haul any excess soil and vegetation removed from site.
- 11) Clean and restore site. Restoration shall include sodding any areas disturbed during construction. Dispose of all construction debris, trash and unused materials.

Ortega St Sidewalk Project




Section A
Approx. 211 feet North of Laredo St
to Olivera St

Section B
Olivera St to Navarre Pkwy

**Section Lengths
(approximate)**

- Section A - 1074 LF
- Section B - 1313 LF
- Total = 2387 LF



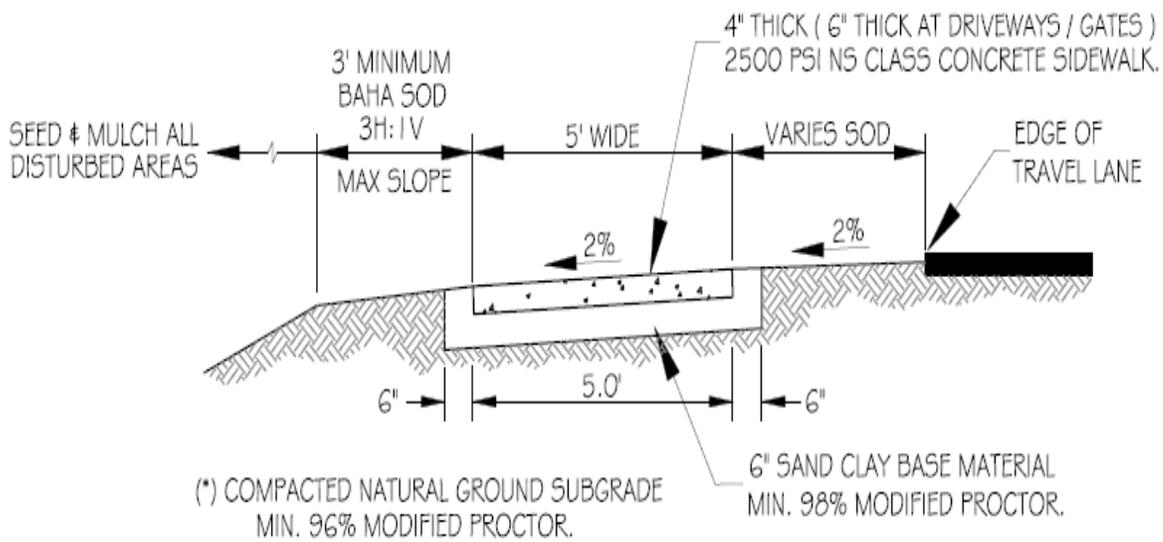

NOTE: REFER TO PLAN SHEETS FOR ADDITIONAL LIMITS OF SODDING AND/OR SEED AND MULCH
TESTING FREQUENCY: ONE (1) DENSITY TEST EACH FOR SUBGRADE AND BASE EVERY 200 LF

5 FOOT WIDE SIDEWALK DETAIL

N.T.S.

1.00 INSTRUCTIONS TO BIDDERS:

A Bid form is included in these specifications. Bid documents shall be sealed and clearly labeled with the words "ITB #16-061 Ortega Street Sidewalk Project", name of bidder and date and time of opening so as to guard against premature opening of any bid. The Owner may consider as informal any bid on which there is an alteration of or departure from the Bid Form hereto attached. The Bid shall be based upon the completion of the work according to the drawings and specifications, together with all addenda thereto.

Evidence of all appropriate required licenses, current Business Tax Receipt, notarized Sworn Statement, and Certificate of Competency shall be attached to the Bid Documents.

2.00 INTERPRETATION:

No oral interpretation will be made to any Bidder as to the meaning of the drawings or specifications. Every interpretation made to a Bidder will be in the form of an Addendum to the specifications. Addenda will be furnished to each Bidder, but it shall be the Bidder's responsibility to make inquiry as to Addenda issued. All such addenda shall become part of the contract and all Bidders shall be bound by such Addenda whether or not received by the Bidders.

3.00 FAMILIARITY WITH LAWS:

It is the Bidder's responsibility to be familiar with all Federal, State, and local laws, ordinances, rules, and regulations that in any manner, affect the work. Ignorance thereof the part of the Bidder will in no way relieve him from responsibility.

4.00 EXAMINATION OF DOCUMENTS AND SITE:

Before submitting his proposal, Bidder shall visit the site of the proposed work and familiarize himself with the nature and extent of the work and any local conditions that may in any manner affect the work to be done and the equipment, materials, and labor required.

He shall also examine the drawings, specifications, and other Contract Documents to inform himself thoroughly regarding any and all conditions and requirements that may in any manner affect the work to be performed under the contract.

5.00 RIGHT TO REJECT PROPOSAL:

The Owner reserves the right to waive informalities in bids to reject any or all bids with or without cause and accept the bid that in its judgment is in the best interest of the County.

6.00 TIME OF COMPLETION:

The entire project shall be completed within ninety (90) calendar days from the Notice To Proceed date.

7.00 FORM OF AGREEMENT:

The Contract form shall be provided by the County Attorney.

8.00 BID GUARANTEE:

Each bid shall be submitted on the bid form provided and must be accompanied by a Certified Check or bid Bond

in the amount of five percent (5%) of the Base Bid, and copies of all required licenses. Such Bid Bond or Check is given with the understanding and agreement that it guarantees: (1) that the bidder will not withdraw his bid for a period of 60 days after the bids have been opened; and, (2) that if his bid is accepted, the Bidder will enter into the written Contract with Santa Rosa County and furnish the required Performance Bond Payment Bond Insurance Certificates, within 10 days after receipt of Notice of Award of his bid. Pursuant to Florida Statutes, Section 255.05, should the contract exceed \$100,000, the Contractor shall be required to execute and record performance and payment bonds. These bonds must state the name and principal business address of both the principal and the surety and a description of the project sufficient to identify it. In the event the bidder fails to comply with any of these conditions and requirements in whole or in part, the full amount of the bond or check shall be automatically forfeited to Santa Rosa County as damages on account of the default of the bidder.

BID FORM

ORTEGA STREET SIDEWALK PROJECT

(To be copied by the Bidder on his own letterhead)

TO: Santa Rosa County Procurement Department
6495 Caroline Street, Suite J
Milton, Florida 32570

REFERENCE: **ITB # 16-061 ORTEGA STREET SIDEWALK PROJECT**

BASE BID PRICE: _____ DATE: _____

Dear Sir:

I have received the Bid Documents consisting of the Project Manual entitled **ORTEGA STREET SIDEWALK PROJECT** prepared by Santa Rosa County Public Works Department, 6075 Old Bagdad Highway, Milton, Florida 32583.

I have also received Addenda Numbers _____ and have included their provisions in my Bid. I have examined both the Bid Documents and the site.

In submitting the Bid, I agree:

1. To hold my bid in full force and effect for a period of sixty (60) calendar days after the time of opening of this Bid.
2. To accept the provisions of the Instructions to Bidders regarding disposition of Bid Guarantee.
3. To enter into and execute a Contract within 10 (ten) calendar days after said Contract is delivered to me, if awarded on the basis of this Bid.
 4. To accomplish the work in accordance with the Contract Documents.
 5. To commence work under this Contract on or before a date to be specified in written "Notice of Proceed" by the County Attorney and to complete project within ninety (90) Calendar days thereafter.
6. To pay as liquidated damages, the sum of \$500.00 for each consecutive calendar day after completion date, as called for in the Contract Agreement as modified.
7. Provide Santa Rosa County with performance bonds and adhere to Supplementary Conditions.

Bid Tabulation		
Ortega Street Sidewalks	Location	Bid (\$)
Section A - Sidewalks	Branston to Olivera Street	
Section B – Sidewalks	Olivera Street to Navarre Parkway	
Base Bid (Sections A & B)	Branston to Navarre Parkway	

I will construct this project for the lump sum price of:

BASE BID _____ (*\$* _____)

FIRM: _____

BY (print): _____

SIGNATURE: _____

TITLE: _____

DATE: _____

MAILING ADDRESS _____

PHONE(____) _____ *FAX* (____) _____

EMAIL _____

NOTE: Please return this bid form to the above address. **NO OTHER BID FORM WILL BE ACCEPTED**

END OF SECTION

SANTA ROSA COUNTY
BOARD OF COUNTY COMMISSIONERS
INSURANCE REQUIREMENTS

INSURANCE REQUIREMENTS

- 1) THE CONTRACTOR SHALL OBTAIN AND MAINTAIN SUCH INSURANCE AS WILL PROTECT IT FROM: (1) CLAIMS UNDER WORKER'S COMPENSATION LAWS, DISABILITY BENEFIT LAWS, OR OTHER SIMILAR EMPLOYEE BENEFIT LAWS; (2) CLAIMS FOR DAMAGES BECAUSE OF BODILY INJURY, OCCUPATIONAL SICKNESS OR DISEASE OR DEATH OF HIS EMPLOYEES INCLUDING CLAIMS INSURED BY USUAL PERSONAL INJURY LIABILITY COVERAGE; (3) CLAIMS FOR DAMAGES BECAUSE OF BODILY INJURY, SICKNESS OR DISEASE, OR DEATH OF ANY PERSON OTHER THAN HIS EMPLOYEES INCLUDING CLAIMS INSURED BY USUAL PERSONAL INJURY LIABILITY COVERAGE; AND (4) FROM CLAIMS FOR INJURY TO OR DESTRUCTION OF TANGIBLE PROPERTY INCLUDING LOSS OR USE RESULTING THEREFROM - - ANY OR ALL OF WHICH CLAIMS MAY ARISE OUT OF, OR RESULT FROM, THE SERVICES, WORK AND OPERATIONS CARRIED OUT PURSUANT TO AND UNDER THE REQUIREMENTS OF THE CONTRACT DOCUMENTS, WHETHER SUCH SERVICES, WORK AND OPERATIONS BE BY THE CONTRACTOR, ITS EMPLOYEES, OR BY SUBCONTRACTOR(S), OR ANYONE EMPLOYED BY OR UNDER THE SUPERVISION OF ANY OF THEM, OR FOR WHOSE ACTS ANY OF THEM MAY BE LEGALLY LIABLE.
- 2) THIS INSURANCE SHALL BE OBTAINED AND WRITTEN FOR NOT LESS THAN THE LIMITS OF LIABILITY SPECIFIED HEREINAFTER, OR AS REQUIRED BY LAW, WHICHEVER IS GREATER.
- 3) THE CONTRACTOR SHALL REQUIRE, AND SHALL BE RESPONSIBLE FOR ASSURING THROUGHOUT THE TIME THE AGREEMENT IS IN EFFECT, THAT ANY AND ALL OF ITS SUBCONTRACTORS OBTAIN AND MAINTAIN UNTIL THE COMPLETION OF THAT SUBCONTRACTOR'S WORK, SUCH OF THE INSURANCE COVERAGES DESCRIBED HEREIN AS ARE REQUIRED BY LAW TO BE PROVIDED ON BEHALF OF THEIR EMPLOYEES AND OTHERS.
- 4) THE CONTRACTOR SHALL REQUIRE THE INSURANCE AGENT/BROKER TO PROVIDE REPLACEMENT CERTIFICATES OF INSURANCE ON A TIMELY BASIS, PREFERABLY NO LATER THAN FIVE (5) DAYS PRIOR TO POLICY TERMINATION.
- 5) THE CONTRACTOR SHALL OBTAIN AND MAINTAIN THE FOLLOWING INSURANCE COVERAGES AS PROVIDED HEREIN BEFORE, AND IN THE TYPE, AMOUNTS AND IN CONFORMANCE WITH THE FOLLOWING MINIMUM REQUIREMENTS:
 - A. FLORIDA STATUTORY WORKERS' COMPENSATION AND EMPLOYERS LIABILITY WITH MINIMUM LIMITS OF \$500,000, WHETHER REQUIRED BY CHAPTER 440, FLORIDA STATUTES OR NOT. IN ADDITION, COVERAGE UNDER THE U. S. LONGSHOREMEN & HARBOR WORKERS' AND JONES ACT, MAY BE REQUIRED COVERAGES BY LAW OR REGULATION FOR THE WORK SPECIFIED IN THIS CONTRACT. CONTRACTOR AND SUBCONTRACTORS MAY PROVIDE A VALID CERTIFICATE OF EXEMPTION ISSUED BY THE STATE OF FLORIDA IN LIEU OF WORKERS' COMPENSATION INSURANCE COVERAGE.

- B. COMMERCIAL GENERAL LIABILITY WITH MINIMUM COMBINED SINGLE LIMITS OF \$1,000,000, INCLUDING COVERAGE PARTS OF BODILY INJURY, BROAD FORM PROPERTY DAMAGE, PERSONAL INJURY, INDEPENDENT CONTRACTORS, BLANKET CONTRACTUAL LIABILITY AND PRODUCTS AND COMPLETED OPERATIONS. THE EXCLUSION FOR UNDERGROUND DAMAGE, EXPLOSION AND COLLAPSE SHALL BE REMOVED THROUGH A POLICY ENDORSEMENT. THE COMMERCIAL GENERAL LIABILITY POLICY'S TOTAL POLLUTION EXCLUSION SHALL BE REMOVED BY ENDORSEMENT. COMPLETED OPERATIONS AND PRODUCTS LIABILITY SHALL BE MAINTAINED FOR A PERIOD OF TWO (2) YEARS AFTER FINAL PAYMENT.
- C. AUTOMOBILE LIABILITY WITH MINIMUM COMBINED SINGLE LIMITS OF \$1,000,000 FOR ALL HIRED, OWNED AND NON-OWNED VEHICLES. THE AUTOMOBILE LIABILITY POLICY'S TOTAL POLLUTION EXCLUSION SHALL BE REMOVED BY ENDORSEMENT.
- D. EXCESS OR UMBRELLA LIABILITY WITH MINIMUM LIMITS OF \$2,000,000 WHICH ARE NO MORE RESTRICTIVE THAN THE UNDERLYING LIMITS. UMBRELLA COVERAGE SHALL DROP DOWN TO PROVIDE COVERAGE WHERE THE UNDERLYING LIMITS ARE EXHAUSTED. THE UMBRELLA POLICY SHALL MIRROR THE COMMERCIAL GENERAL AND AUTOMOBILE POLICIES' COVERAGE WITH RESPECT TO REMOVAL OF THE TOTAL POLLUTION EXCLUSION.
- E. PROFESSIONAL LIABILITY INSURANCE WITH MINIMUM LIMITS OF \$500,000 FOR ENGINEERS AND ARCHITECTS EMPLOYED BY THE CONTRACTOR, IF ANY.
- F. BUILDERS RISK INSURANCE UNDERWRITTEN ON THE "ALL RISKS OF PHYSICAL LOSS" BASIS FOR REPLACEMENT COST FOR THE FULL VALUE OF THE COMPLETED PROJECT TO COVER THE OWNER AND CONTRACTOR AS THEIR INTEREST MAY APPEAR. AN INSTALLATION FLOATER MAY BE AN ALTERNATIVE IF APPROPRIATE TO THIS SPECIFIC CONTRACT.
- G. CONTRACTOR SHALL PROCURE AND FURNISH OWNER'S PROTECTION LIABILITY INSURANCE POLICY NAMING SANTA ROSA COUNTY WITH THE FOLLOWING LIMITS:
 - 1. \$1,000,000 PER OCCURRENCE.
 - 2. \$2,000,000 AGGREGATE.

ARTICLE 1 GENERAL PROVISIONS

1.1 BASIC DEFINITIONS

1.1.1 THE CONTRACT DOCUMENTS

The Contract Documents consist of the Agreement between Owner and Contractor (hereinafter the Agreement), Conditions of the Contract (General, Supplementary and other Conditions), Drawings/maps/sketches, Specifications, Addenda issued prior to execution of the Contract, other documents listed in the Agreement and Modifications issued after execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties, (2) a Change Order, (3) a Construction Change Directive or (4) a written order for a minor change in the Work issued by the Engineer. Unless specifically enumerated in the Agreement, the Contract Documents do not include other documents such as bidding requirements (advertisement or invitation to bid, Instructions to Bidders, sample forms, the Contractor's bid or portions of Addenda relating to bidding requirements).

1.1.2 THE CONTRACT

The Contract Documents form the Contract for Construction. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations or agreements, either written or oral. The Contract may be amended or modified only by a Modification. The Contract Documents shall not be construed to create a contractual relationship of any kind (1) between the Engineer and Contractor, (2) between the Owner and a Subcontractor or Sub-Subcontractor, (3) between the Owner and Engineer or (4) between any persons or entities other than the Owner and Contractor. The Engineer shall, however, be entitled to performance and enforcement of obligations under the Contract intended to facilitate performance of the Engineer's duties.

1.1.3 THE WORK

The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or a part of the Project.

1.1.4 THE PROJECT

The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by the Owner or by separate Contractors.

1.1.5 THE DRAWINGS

The Drawings are the graphic and pictorial portions of the Contract Documents showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules and diagrams.

1.1.6 THE SPECIFICATIONS

The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, systems, standards and workmanship for the Work, and performance of related services.

1.1.7 THE PROJECT MANUAL

The Project Manual is a volume assembled for the Work which may include the bidding requirements, sample forms, Conditions of the Contract and Specifications.

1.2 CORRELATION AND INTENT OF THE CONTRACT DOCUMENTS

1.2.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all; performance by the Contractor shall be required only to the extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the indicated results.

1.2.2 Organization of the Specifications into divisions, sections and articles, and arrangement of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in

establishing the extent of Work to be performed by any trade.

1.2.3 Unless otherwise stated in the Contract Documents, words which have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings.

1.3 CAPITALIZATION

1.3.1 Terms capitalized in these General Conditions include those which are (1) specifically defined, (2) the titles of numbered articles and identified references to Paragraphs, Subparagraphs and Clauses in the document.

1.4 INTERPRETATION

1.4.1 In the interest of brevity the Contract Documents frequently omit modifying words such as “all” and “any” and articles such as “the” and “an”, but the fact that a modifier or an article is absent from one statement and appears in another is not intended to affect the interpretation of either statement.

1.5 EXECUTION OF CONTRACT DOCUMENTS

1.5.1 The Contract Documents shall be signed by the Owner and Contractor. If either the Owner or Contractor or both do not sign all the Contract Documents, the Engineer shall identify such unsigned Documents upon request.

1.5.2 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become generally familiar with local conditions under which the Work is to be performed and correlated personal observations with requirements of the Contract Documents.

1.6 OWNERSHIP AND USE OF DRAWINGS/MAPS/SKETCHES, SPECIFICATIONS AND OTHER INSTRUMENTS OF SERVICE

1.6.1 The Drawings/maps/sketches, Specifications and other documents, including those in electronic form, prepared by the Engineer and the Engineer's consultants are Instruments of Service through which the Work to be executed by the Contractor is described. The Contractor may retain one record set. Neither the Contractor nor any Subcontractor, Sub-Subcontractor or material or equipment supplier shall own or claim a copyright in the Drawings, Specifications and other documents prepared by the Engineer or the Engineer's consultants, and unless otherwise indicated the Engineer and the Engineer's consultants shall be deemed the authors of them and will retain all common law, statutory and other reserved rights, in addition to the copyrights. All copies of Instruments of Service, except the Contractor's record set, shall be returned or suitably accounted for to the Engineer, on request, upon completion of the Work. The Drawings, Specifications and other documents prepared by the Engineer and the Engineer's consultants, and copies thereof furnished to the Contractor, are for use solely with respect to this Project. They are not to be used by the Contractor or any Subcontractor, Sub- Subcontractor or material or equipment supplier on other projects or for additions to this Project outside the scope of the Work without the specific written consent of the Owner, Engineer and the Engineer's consultants. The Contractor, Subcontractors, Sub-Subcontractors and material or equipment suppliers are authorized to use and reproduce applicable portions of the Drawings, Specifications and other documents prepared by the Engineer and the Engineer's consultants appropriate to and for use in the execution of their Work under the Contract Documents. All copies made under this authorization shall bear the statutory copyright notice, if any, shown on the Drawings, Specifications and other documents prepared by the Engineer and the Engineer's consultants. Submittal or distribution to meet official regulatory requirements or for other purposes in connection with this Project is not to be construed as publication in derogation of the Engineer's or Engineer's consultants' copyrights or other reserved rights.

ARTICLE 2 OWNER

2.1 GENERAL

2.1.1 The Owner is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Owner shall designate in writing a representative who shall have express authority to bind the Owner with respect to all matters requiring the Owner's approval or authorization. Except as otherwise provided in Subparagraph **4.2.1**, the Engineer does not have such authority. The term "Owner" means the Owner or the Owner's authorized representative.

2.1.2 The Owner shall furnish to the Contractor within fifteen days after receipt of a written request, information necessary and relevant for the Contractor to evaluate, give notice of or enforce mechanic's lien rights. Such information shall include a correct statement of the record legal title to the property on which the Project is located, usually referred to as the site, and the Owner's interest therein.

2.2 INFORMATION AND SERVICES REQUIRED OF THE OWNER

2.2.1 The Owner shall, at the written request of the Contractor, prior to commencement of the Work and thereafter, furnish to the Contractor reasonable evidence that financial arrangements have been made to fulfill the Owner's obligations under the Contract. Furnishing of such evidence shall be a condition precedent to commencement or continuation of the Work. After such evidence has been furnished, the Owner shall not materially vary such financial arrangements without prior notice to the Contractor.

2.2.2 Except for permits and fees, including those required under Subparagraph **3.7.1**, which are the responsibility of the Contractor under the Contract Documents, the Owner shall secure and pay for necessary approvals, easements, assessments and charges required for construction, use or occupancy of permanent structures or for permanent changes in existing facilities.

2.2.3 The Owner shall furnish surveys describing physical characteristics, legal limitations and utility locations for the site of the Project, and a legal description of the site. The Contractor shall be entitled to rely on the accuracy of information furnished by the Owner but shall exercise proper precautions relating to the safe performance of the Work.

2.2.4 Information or services required of the Owner by the Contract Documents shall be furnished by the Owner with reasonable promptness. Any other information or services relevant to the Contractor's performance of the Work under the Owner's control shall be furnished by the Owner after receipt from the Contractor of a written request for such information or services.

2.2.5 Unless otherwise provided in the Contract Documents, the Contractor will be furnished, free of charge, such copies of Drawings and Project Manuals as are reasonably necessary for execution of the Work.

2.3 OWNER'S RIGHT TO STOP THE WORK

2.3.1 If the Contractor fails to correct Work which is not in accordance with the requirements of the Contract Documents as required by Paragraph **12.2** or persistently fails to carry out Work in accordance with the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Subparagraph **6.1.3**.

2.4 OWNER'S RIGHT TO CARRY OUT THE WORK

2.4.1 If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a seven-day period after receipt of written notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may after such seven-day period give the Contractor a second written notice to correct such deficiencies within a three-day period. If the Contractor within such three-day period after receipt of such second notice fails to commence and continue to correct any deficiencies, the Owner may, without prejudice to other remedies the Owner may have, correct such deficiencies. In such case an

appropriate Change Order shall be issued deducting from payments then or thereafter due the Contractor the reasonable cost of correcting such deficiencies, including Owner's expenses and compensation for the Engineer's additional services made necessary by such default, neglect or failure. Such action by the Owner and amounts charged to the Contractor are both subject to prior approval of the Engineer. If payments then or thereafter due the Contractor are not sufficient to cover such amounts, the Contractor shall pay the difference to the Owner.

ARTICLE 3 CONTRACTOR

3.1 GENERAL

3.1.1 The Contractor is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The term "Contractor" means the Contractor or the Contractor's authorized representative.

3.1.2 The Contractor shall perform the Work in accordance with the Contract Documents.

3.1.3 The Contractor shall not be relieved of obligations to perform the Work in accordance with the Contract Documents either by activities or duties of the Engineer in the Engineer's administration of the Contract, or by tests, inspections or approvals required or performed by persons other than the Contractor.

3.2 REVIEW OF CONTRACT DOCUMENTS AND FIELD CONDITIONS BY CONTRACTOR

3.2.1 Since the Contract Documents are complementary, before starting each portion of the Work, the Contractor shall carefully study and compare the various Drawings and other Contract Documents relative to that portion of the Work, as well as the information furnished by the Owner pursuant to Subparagraph **2.2.3**, shall take field measurements of any existing conditions related to that portion of the Work and shall observe any conditions at the site affecting it. These obligations are for the purpose of facilitating construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however, any errors, inconsistencies or omissions discovered by the Contractor shall be reported promptly to the Engineer as a request for information in such form as the Engineer may require.

3.2.2 Any design errors or omissions noted by the Contractor during this review shall be reported promptly to the Engineer, but it is recognized that the Contractor's review is made in the Contractor's capacity as a Contractor and not as a licensed design professional unless otherwise specifically provided in the Contract Documents. The Contractor is not required to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, building codes, and rules and regulations, but any nonconformity discovered by or made known to the Contractor shall be reported promptly to the Engineer.

3.2.3 If the Contractor believes that additional cost or time is involved because of clarifications or instructions issued by the Engineer in response to the Contractor's notices or requests for information pursuant to Subparagraphs **3.2.1** and **3.2.2**, the Contractor shall make Claims as provided in Subparagraphs **4.3.6** and **4.3.7**. If the Contractor fails to perform the obligations of Subparagraphs **3.2.1** and **3.2.2**, the Contractor shall pay such costs and damages to the Owner as would have been avoided if the Contractor had performed such obligations. The Contractor shall not be liable to the Owner or Engineer for damages resulting from errors, inconsistencies or omissions in the Contract Documents or for differences between field measurements or conditions and the Contract Documents unless the Contractor recognized such error, inconsistency, omission or difference and knowingly failed to report it to the Engineer.

3.3 SUPERVISION AND CONSTRUCTION PROCEDURES

3.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for and have control over construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract, unless the Contract Documents give other specific instructions concerning these matters. If the Contract Documents give specific instructions concerning construction means, methods, techniques, sequences or procedures, the Contractor shall evaluate the jobsite safety thereof and, except as stated below, shall be fully and solely responsible for the jobsite safety of such means, methods, techniques, sequences or procedures. If the Contractor determines that such means, methods, techniques, sequences or procedures may not be safe, the Contractor shall give timely written notice to the Owner and Engineer and shall not proceed with that portion of the Work without further written instructions from the Engineer. If the Contractor is then instructed to proceed with the required means, methods, techniques, sequences or procedures without acceptance of changes proposed by the Contractor, the Owner shall be solely responsible for any resulting loss or damage.

3.3.2 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for or on behalf of the Contractor or any of its Subcontractors.

3.3.3 The Contractor shall be responsible for inspection of portions of Work already performed to determine that such portions are in proper condition to receive subsequent Work.

3.4 LABOR AND MATERIALS

3.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

3.4.2 The Contractor may make substitutions only with the consent of the Owner, after evaluation by the Engineer and in accordance with a Change Order.

3.4.3 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Contract. The Contractor shall not permit employment of unfit persons or persons not skilled in tasks assigned to them.

3.5 WARRANTY

3.5.1 The Contractor warrants to the Owner and Engineer that materials and equipment furnished under the Contract will be of good quality and new unless otherwise required or permitted by the Contract Documents, that the Work will be free from defects not inherent in the quality required or permitted, and that the Work will conform to the requirements of the Contract Documents. Work not conforming to these requirements, including substitutions not properly approved and authorized, may be considered defective. The Contractor's warranty excludes remedy for damage or defect caused by abuse, modifications not executed by the Contractor, improper or insufficient maintenance, improper operation, or normal wear and tear and normal usage. If required by the Engineer, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment.

3.6 TAX

3.6.1 The Contractor shall pay sales, consumer, use and similar taxes for the Work provided by the Contractor which are legally enacted when bids are received or negotiations concluded, whether or not yet effective or merely scheduled to go into effect.

3.7 PERMITS, FEES AND NOTICES

3.7.1 Unless otherwise provided in the Contract Documents, the Contractor shall secure and pay for the building permit and other permits and governmental fees, licenses and inspections necessary for proper execution and completion of the Work which are customarily secured after execution of the Contract and which are legally required when bids are received or negotiations concluded.

3.7.2 The Contractor shall comply with and give notices required by laws, ordinances, rules, regulations and lawful orders of public authorities applicable to performance of the Work.

3.7.3 It is not the Contractor's responsibility to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, building codes, and rules and regulations. However, if the Contractor observes that portions of the Contract Documents are at variance therewith, the Contractor shall promptly notify the Engineer and Owner in writing, and necessary changes shall be accomplished by appropriate Modification.

3.7.4 If the Contractor performs Work knowing it to be contrary to laws, statutes, ordinances, building codes, and rules and regulations without such notice to the Engineer and Owner, the Contractor shall assume appropriate responsibility for such Work and shall bear the costs attributable to correction.

3.8 ALLOWANCES

3.8.1 The Contractor shall include in the Contract Sum all allowances stated in the Contract Documents. Items covered by allowances shall be supplied for such amounts and by such persons

or entities as the Owner may direct, but the Contractor shall not be required to employ persons or entities to whom the Contractor has reasonable objection.

3.8.2 Unless otherwise provided in the Contract Documents:

- 1 allowances shall cover the cost to the Contractor of materials and equipment delivered at the site and all required taxes, less applicable trade discounts;
- 2 Contractor's costs for unloading and handling at the site, labor, installation costs, overhead, profit and other expenses contemplated for stated allowance amounts shall be included in the Contract Sum but not in the allowances;
- 3 whenever costs are more than or less than allowances, the Contract Sum shall be adjusted accordingly by Change Order. The amount of the Change Order shall reflect (1) the difference between actual costs and the allowances under Clause **3.8.2.1** and (2) changes in Contractor's costs under Clause **3.8.2.2**.

3.8.3 Materials and equipment under an allowance shall be selected by the Owner in sufficient time to avoid delay in the Work.

3.9 SUPERINTENDENT

3.9.1 The Contractor shall employ competent superintendent and necessary assistants who shall be in attendance at the Project site during performance of the Work. The superintendent shall represent the Contractor, and communications given to the superintendent shall be as binding as if given to the Contractor. Important communications shall be confirmed in writing. Other communications shall be similarly confirmed on written request in each case.

3.10 CONTRACTOR'S CONSTRUCTION SCHEDULES

3.10.1 The Contractor, promptly after being awarded the Contract, shall prepare and submit for prior approval by Owner and Engineer Contractor's construction schedule for the Work. The schedule shall not exceed time limits current under the Contract Documents, shall be revised at appropriate intervals as required by the conditions of the Work and Project, shall be related to the entire Project to the extent required by the Contract Documents, and shall provide for expeditious and practicable execution of the Work.

3.10.2 The Contractor shall prepare and keep current, for the Engineer's approval, a schedule of submittals which is coordinated with the Contractor's construction schedule and allows the Engineer reasonable time to review submittals.

3.10.3 The Contractor shall perform the Work in general accordance with the most recent schedules submitted to the Owner and Engineer.

3.11 DOCUMENTS AND SAMPLES AT THE SITE

3.11.1 The Contractor shall maintain at the site for the Owner one record copy of the Drawings, Specifications, Addenda, Change Orders and other Modifications, in good order and marked currently to record field changes and selections made during construction, and one record copy of approved Shop Drawings, Product Data, Samples and similar required submittals. These shall be available to the Engineer and shall be delivered to the Engineer for submittal to the Owner upon completion of the Work.

3.12 SHOP DRAWINGS, PRODUCT DATA AND SAMPLES

3.12.1 Shop Drawings are drawings, diagrams, schedules and other data specially prepared for the Work by the Contractor or a Subcontractor, Sub-Subcontractor, manufacturer, supplier or distributor to illustrate some portion of the Work.

3.12.2 Product Data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams and other information furnished by the Contractor to illustrate materials or equipment for some portion of the Work.

3.12.3 Samples are physical examples which illustrate materials, equipment or workmanship and establish standards by which the Work will be judged.

3.12.4 Shop Drawings, Product Data, Samples, and similar submittals are not Contract Documents.

The purpose of their submittal is to demonstrate for those portions of the Work for which submittals are required by the Contract Documents the way by which the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents. Review by the Engineer is subject to the limitations of Subparagraph 4.2.7. Informational submittals upon which the Engineer is not expected to take responsive action may be so identified in the Contract Documents. Submittals which are not required by the Contract Documents may be returned by the Engineer without action.

- 3.12.5** The Contractor shall review for compliance with the Contract Documents, approve and submit to the Engineer Shop Drawings, Product Data, Samples, and similar submittals required by the Contract Documents with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of the Owner or of separate Contractors. Submittals which are not marked as reviewed for compliance with the Contract Documents and approved by the Contractor may be returned by the Engineer without action.
- 3.12.6** By approving and submitting Shop Drawings, Product Data, Samples, and similar submittals, the Contractor represents that the Contractor has determined and verified materials, field measurements and field construction criteria related thereto, or will do so, and has checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents.
- 3.12.7** The Contractor shall perform no portion of the Work for which the Contract Documents require submittal and review of Shop Drawings, Product Data, Samples, or similar submittals until the respective submittal has been approved by the Engineer.
- 3.12.8** The Work shall be in accordance with approved submittals except that the Contractor shall not be relieved of responsibility for deviations from requirements of the Contract Documents by the Engineer's approval of Shop Drawings, Product Data, Samples, or similar submittals unless the Contractor has specifically informed the Engineer in writing of such deviation at the time of submittal and (1) the Engineer has given written approval to the specific deviation as a minor change in the Work, or (2) a Change Order or Construction Change Directive has been issued authorizing the deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples, or similar submittals by the Engineer's approval thereof.
- 3.12.9** The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data, Samples, or similar submittals, to revisions other than those requested by the Engineer on previous submittals. In the absence of such written notice the Engineer's approval of a resubmission shall not apply to such revisions.
- 3.12.10** The Contractor shall not be required to provide professional services which constitute the practice of Engineering or engineering unless such services are specifically required by the Contract Documents for a portion of the Work or unless the Contractor needs to provide such services in order to carry out the Contractor's responsibilities for construction means, methods, techniques, sequences and procedures. The Contractor shall not be required to provide professional services in violation of applicable law. If professional design services or certifications by a design professional related to systems, materials or equipment are specifically required of the Contractor by the Contract Documents, the Owner and the Engineer will specify all performance and design criteria that such services must satisfy. The Contractor shall cause such services or certifications to be provided by a properly licensed design professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to the Engineer. The Owner and the Engineer shall be entitled to rely upon the adequacy, accuracy and completeness of the services, certifications or approvals performed by such design professionals, provided the Owner and Engineer have specified to the Contractor all performance and design criteria that such services must satisfy. Pursuant to this Subparagraph 3.12.10, the Engineer will review, approve or take other appropriate action on

submittals only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Contractor shall not be responsible for the adequacy of the performance or design criteria required by the Contract Documents.

3.13 USE OF SITE

3.13.1 The Contractor shall confine operations at the site to areas permitted by law, ordinances, permits and the Contract Documents and shall not unreasonably encumber the site with materials or equipment.

3.14 CUTTING AND PATCHING

3.14.1 The Contractor shall be responsible for cutting, fitting or patching required to complete the Work or to make its parts fit together properly.

3.14.2 The Contractor shall not damage or endanger a portion of the Work or fully or partially completed construction of the Owner or separate Contractors by cutting, patching or otherwise altering such construction, or by excavation. The Contractor shall not cut or otherwise alter such construction by the Owner or a separate Contractor except with written consent of the Owner and of such separate Contractor; such consent shall not be unreasonably withheld. The Contractor shall not unreasonably withhold from the Owner or a separate Contractor the Contractor's consent to cutting or otherwise altering the Work.

3.15 CLEANING UP

3.15.1 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials or rubbish caused by operations under the Contract. At completion of the Work, the Contractor shall remove from and about the Project waste materials, rubbish, the Contractor's tools, construction equipment, machinery and surplus materials.

3.15.2 If the Contractor fails to clean up as provided in the Contract Documents, the Owner may do so and the cost thereof shall be charged to the Contractor.

3.16 ACCESS TO WORK

3.16.1 The Contractor shall provide the Owner and Engineer access to the Work in preparation and progress wherever located.

3.17 ROYALTIES, PATENTS AND COPYRIGHTS

3.17.1 The Contractor shall pay all royalties and license fees. The Contractor shall defend suits or claims for infringement of copyrights and patent rights and shall hold the Owner and Engineer harmless from loss on account thereof, but shall not be responsible for such defense or loss when a particular design, process or product of a particular manufacturer or manufacturers is required by the Contract documents or where the copyright violations are contained in Drawings, Specifications or other documents prepared by the Owner or Engineer. However, if the Contractor has reason to believe that the required design, process or product is an infringement of a copyright or a patent, the Contractor shall be responsible for such loss unless such information is promptly furnished to the Engineer.

3.18 INDEMNIFICATION

3.18.1 To the fullest extent permitted by law and to the extent claims, damages, losses or expenses are not covered by Project Management Protective Liability insurance purchased by the Contractor in accordance with Article 11, the Contractor shall indemnify and hold harmless the Owner, Engineer, Engineer's consultants, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), but only to the extent caused by the negligent acts or omissions of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss or expense is caused in part by a party indemnified hereunder. Such obligation shall not be construed to negate, abridge, or reduce other rights or obligations of indemnity which would otherwise exist as to a party or person described in this Paragraph 3.18.

3.18.2 In claims against any person or entity indemnified under this Paragraph **3.18** by an employee of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, the indemnification obligation under Subparagraph **3.18.1** shall not be limited by a limitation on amount or type of damages, compensation or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefit acts or other employee benefit acts.

ARTICLE 4 ADMINISTRATION OF THE CONTRACT

4.1 ENGINEER

4.1.1 The Engineer is the person lawfully licensed to practice Engineerure or an entity lawfully practicing Engineerure identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The term "Engineer" means the Engineer or the Engineer's authorized representative.

4.1.2 Duties, responsibilities and limitations of authority of the Engineer as set forth in the Contract Documents shall not be restricted, modified or extended without written consent of the Owner, Contractor and Engineer. Consent shall not be unreasonably withheld.

4.1.3 If the employment of the Engineer is terminated, the Owner shall employ a new Engineer against whom the Contractor has no reasonable objection and whose status under the Contract Documents shall be that of the former Engineer.

4.2 ENGINEER'S ADMINISTRATION OF THE CONTRACT

4.2.1 The Engineer will provide administration of the Contract as described in the Contract Documents, and will be an Owner's representative (1) during construction, (2) until final payment is due and (3) with the Owner's concurrence, from time to time during the one-year period for correction of Work described in Paragraph **12.2**. The Engineer will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents, unless otherwise modified in writing in accordance with other provisions of the Contract.

4.2.2 The Engineer, as a representative of the Owner, will visit the site at intervals appropriate to the stage of the Contractor's operations (1) to become generally familiar with and to keep the Owner informed about the progress and quality of the portion of the Work completed, (2) to endeavor to guard the Owner against defects and deficiencies in the Work, and (3) to determine in general if the Work is being performed in a manner indicating that the Work, when fully completed, will be in accordance with the Contract Documents. However, the Engineer will not be required to make exhaustive or continuous on-site inspections to check the quality or quantity of the Work. The Engineer will neither have control over or charge of, nor be responsible for, the construction means, methods, techniques, sequences or procedures, or for the safety precautions and programs in connection with the Work, since these are solely the Contractor's rights and responsibilities under the Contract Documents, except as provided in Subparagraph **3.3.1**.

4.2.3 The Engineer will not be responsible for the Contractor's failure to perform the Work in accordance with the requirements of the Contract Documents. The Engineer will not have control over or charge of and will not be responsible for acts or omissions of the Contractor, Subcontractors, or their agents or employees, or any other persons or entities performing portions of the Work.

4.2.4 Communications Facilitating Contract Administration. Except as otherwise provided in the Contract Documents or when direct communications have been specially authorized, the Owner and Contractor shall endeavor to communicate with each other through the Engineer about matters arising out of or relating to the Contract. Communications by and with the Engineer's consultants shall be through the Engineer. Communications by and with Subcontractors and material suppliers shall be through the Contractor. Communications by and with separate Contractors shall be through the Owner.

- 4.2.5** Based on the Engineer's evaluations of the Contractor's Applications for Payment, the Engineer will review and certify the amounts due the Contractor and will issue Certificates for Payment in such amounts.
- 4.2.6** The Engineer will have authority to reject Work that does not conform to the Contract Documents. Whenever the Engineer considers it necessary or advisable, the Engineer will have authority to require inspection or testing of the Work in accordance with Subparagraphs **13.5.2** and **13.5.3**, whether or not such Work is fabricated, installed or completed. However, neither this authority of the Engineer nor a decision made in good faith either to exercise or not to exercise such authority shall give rise to a duty or responsibility of the Engineer to the Contractor, Subcontractors, material and equipment suppliers, their agents or employees, or other persons or entities performing portions of the Work.
- 4.2.7** The Engineer will review and approve or take other appropriate action upon the Contractor's submittals such as Shop Drawings, Product Data and Samples, but only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Engineer's action will be taken with such reasonable promptness as to cause no delay in the Work or in the activities of the Owner, Contractor or separate Contractors, while allowing sufficient time in the Engineer's professional judgment to permit adequate review. Review of such submittals is not conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities, or for substantiating instructions for installation or performance of equipment or systems, all of which remain the responsibility of the Contractor as required by the Contract Documents. The Engineer's review of the Contractor's submittals shall not relieve the Contractor of the obligations under Paragraphs **3.3**, **3.5** and **3.12**. The Engineer's review shall not constitute approval of safety precautions or, unless otherwise specifically stated by the Engineer, of any construction means, methods, techniques, sequences or procedures. The Engineer's approval of a specific item shall not indicate approval of an assembly of which the item is a component.
- 4.2.8** The Engineer will prepare Change Orders and Construction Change Directives, and may authorize minor changes in the Work as provided in Paragraph **7.4**.
- 4.2.9** The Engineer will conduct inspections to determine the date or dates of Substantial Completion and the date of final completion, will receive and forward to the Owner, for the Owner's review and records, written warranties and related documents required by the Contract and assembled by the Contractor, and will issue a final Certificate for Payment upon compliance with the requirements of the Contract Documents.
- 4.2.10** If the Owner and Engineer agree, the Engineer will provide one or more project representatives to assist in carrying out the Engineer's responsibilities at the site. The duties, responsibilities and limitations of authority of such project representatives shall be as set forth in an exhibit to be incorporated in the Contract Documents.
- 4.2.11** The Engineer will interpret and decide matters concerning performance under, and requirements of, the Contract Documents on written request of either the Owner or Contractor. The Engineer's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness. If no agreement is made concerning the time within which interpretations required of the Engineer shall be furnished in compliance with this Paragraph **4.2**, then delay shall not be recognized on account of failure by the Engineer to furnish such interpretations until **15** days after written request is made for them.
- 4.2.12** Interpretations and decisions of the Engineer will be consistent with the intent of and reasonably inferable from the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and initial decisions, the Engineer will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either and will not be liable for results of interpretations or decisions so rendered in good faith.
- 4.2.13** The Engineer's decisions on matters relating to aesthetic effect will be final if consistent with the intent expressed in the Contract Documents.

4.3 CLAIMS AND DISPUTES

4.3.1 Definition. A Claim is a demand or assertion by one of the parties seeking, as a matter of right, adjustment or interpretation of Contract terms, payment of money, extension of time or other relief with respect to the terms of the Contract. The term "Claim" also includes other disputes and matters in question between the Owner and Contractor arising out of or relating to the Contract. Claims must be initiated by written notice. The responsibility to substantiate claims shall rest with the party making the Claim.

4.3.2 Time Limits on Claims. Claims by either party must be initiated within **21** days after occurrence of the event giving rise to such Claim or within **21** days after the claimant first recognizes the condition giving rise to the Claim, whichever is later. Claims must be initiated by written notice to the Engineer and the other party.

4.3.3 Continuing Contract Performance. Pending final resolution of a Claim except as otherwise agreed in writing or as provided in Subparagraph **9.7.1** and Article **14**, the Contractor shall proceed diligently with performance of the Contract and the Owner shall continue to make payments in accordance with the Contract Documents.

4.3.4 Claims for Concealed or Unknown Conditions. If conditions are encountered at the site which are (1) subsurface or otherwise concealed physical conditions which differ materially from those indicated in the Contract Documents or (2) unknown physical conditions of an unusual nature, which differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, then notice by the observing party shall be given to the other party promptly before Conditions are disturbed and in no event later than **21** days after first observance of the conditions. The Engineer will promptly investigate such conditions and, if they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend an equitable adjustment in the Contract Sum or Contract Time, or both. If the Engineer determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Engineer shall so notify the Owner and Contractor in writing, stating the reasons. Claims by either party in opposition to such determination must be made within **21** days after the Engineer has given notice of the decision. If the conditions encountered are materially different, the Contract Sum and Contract Time shall be equitably adjusted, but if the Owner and Contractor cannot agree on an adjustment in the Contract Sum or Contract Time, the adjustment shall be referred to the Engineer for initial determination, subject to further proceedings pursuant to Paragraph **4.4**.

4.3.5 Claims for Additional Cost. If the Contractor wishes to make Claim for an increase in the Contract Sum, written notice as provided herein shall be given before proceeding to execute the Work. Prior notice is not required for Claims relating to an emergency endangering life or property arising under Paragraph **10.6**.

4.3.6 If the Contractor believes additional cost is involved for reasons including but not limited to (1) a written interpretation from the Engineer, (2) an order by the Owner to stop the Work where the Contractor was not at fault, (3) a written order for a minor change in the Work issued by the Engineer, (4) failure of payment by the Owner, (5) termination of the Contract by the Owner, (6) Owner's suspension or (7) other reasonable grounds, Claim shall be filed in accordance with this Paragraph **4.3**.

4.3.7 CLAIMS FOR ADDITIONAL TIME

4.3.7.1 If the Contractor wishes to make Claim for an increase in the Contract Time, written notice as provided herein shall be given. The Contractor's Claim shall include an estimate of cost and of probable effect of delay on progress of the Work. In the case of a continuing delay only one Claim is necessary.

4.3.7.2 If adverse weather conditions are the basis for a Claim for additional time, such Claim shall be documented by data substantiating that weather conditions were abnormal for the period of time, could not have been reasonably anticipated and had an adverse effect on the scheduled construction.

4.3.8 Injury or Damage to Person or Property. If either party to the Contract suffers injury or damage to person or property because of an act or omission of the other party, or of others for whose acts such party is legally responsible, written notice of such injury or damage, whether or not insured, shall be given to the other party within a reasonable time not exceeding **21** days after discovery. The notice shall provide sufficient detail to enable the other party to investigate the matter.

4.3.9 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed in a proposed Change Order or Construction Change Directive so that application of such unit prices to quantities of Work proposed will cause substantial inequity to the Owner or Contractor, the applicable unit prices shall be equitably adjusted.

4.3.10 Claims for Consequential Damages. The Contractor and Owner waive Claims against each other for consequential damages arising out of or relating to this Contract. This mutual waiver includes:

- 1** damages incurred by the Owner for rental expenses, for losses of use, income, profit, financing, business and reputation, and for loss of management or employee productivity or of the services of such persons; and
- 2** damages incurred by the Contractor for principal office expenses including the compensation of personnel stationed there, for losses of financing, business and reputation, and for loss of profit except anticipated profit arising directly from the Work.

This mutual waiver is applicable, without limitation, to all consequential damages due to either party's termination in accordance with Article **14**. Nothing contained in this Subparagraph **4.3.10** shall be deemed to preclude an award of liquidated direct damages, when applicable, in accordance with the requirements of the Contract Documents.

4.4 RESOLUTION OF CLAIMS AND DISPUTES

4.4.1 The Engineer will review Claims and take one or more of the following preliminary actions within ten days of receipt of a Claim: (1) request additional supporting data from the claimant; (2) submit a schedule to the parties indicating when the Engineer expects to take action; (3) reject the Claim in whole or in part stating reasons for rejection; (4) recommend approval of the Claim by the other party; or (5) suggest a compromise. The Engineer may also, but is not obligated to, notify the surety, if any, of the nature and amount of the Claim.

4.4.2 If a Claim has been resolved, the Engineer will prepare or obtain appropriate documentation.

4.4.3 If a Claim has not been resolved, the party making the Claim shall, within ten days after the Engineer's preliminary response take one or more of the following actions: (1) submit additional supporting data requested by the Engineer; (2) modify the initial Claim; or (3) notify the Engineer that the initial Claim stands.

4.4.4 If a Claim has not been resolved after consideration of the foregoing and of further evidence presented by the parties or requested by the Engineer, the Engineer will notify the parties in writing that the Engineer's decision will be made within seven days, which decision shall be final and binding on the parties. Upon expiration of such time period, the Engineer will render to the parties the Engineer's written decision relative to the Claim, including any change in the Contract Sum or Contract Time or both. If there is a surety and there appears to be a possibility of a Contractor's default, the Engineer may, but is not obligated to, notify the surety and request the surety's assistance in resolving the controversy.

ARTICLE 5 SUBCONTRACTORS

5.1 DEFINITIONS

5.1.1 A Subcontractor is a person or entity who has a direct contract with the Contractor to perform a portion of the Work at the site. The term "Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Subcontractor or an authorized representative of the Subcontractor. The term "Subcontractor" does not include a separate Contractor or Subcontractors of a separate Contractor.

5.1.2 A Sub-Subcontractor is a person or entity who has a direct or indirect contract with a Subcontractor to perform a portion of the Work at the site. The term "Sub-Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Sub-Subcontractor or an authorized representative of the Sub-Subcontractor.

5.2 AWARD OF SUBCONTRACTS AND OTHER CONTRACTS FOR PORTIONS OF THE WORK

5.2.1 Unless otherwise stated in the Contract Documents or the bidding requirements, the Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Owner through the Engineer the names of persons or entities (including those who are to furnish materials or equipment fabricated to a special design) proposed for each principal portion of the Work. The Engineer will promptly reply to the Contractor in writing stating whether or not the Owner or the Engineer, after due investigation, has reasonable objection to any such proposed person or entity. Failure of the Owner or Engineer to reply promptly shall constitute notice of no reasonable objection.

5.2.2 The Contractor shall not contract with a proposed person or entity to whom the Owner or Engineer has made reasonable and timely objection. The Contractor shall not be required to contract with anyone to whom the Contractor has made reasonable objection.

5.2.3 If the Owner or Engineer has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner or Engineer has no reasonable objection. If the proposed but rejected Subcontractor was reasonably capable of performing the Work, the Contract Sum and Contract Time shall be increased or decreased by the difference, if any, occasioned by such change, and an appropriate Change Order shall be issued before commencement of the substitute Subcontractor's Work. However, no increase in the Contract Sum or Contract Time shall be allowed for such change unless the Contractor has acted promptly and responsively in submitting names as required.

5.2.4 The Contractor shall not change a Subcontractor, person or entity previously selected if the Owner or Engineer makes reasonable objection to such substitute.

5.3 SUBCONTRACTUAL RELATIONS

5.3.1 By appropriate agreement, written where legally required for validity, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by terms of the Contract Documents, and to assume toward the Contractor all the obligations and responsibilities, including the responsibility for safety of the Subcontractor's Work, which the Contractor, by these Documents, assumes toward the Owner and Engineer. Each subcontract agreement shall preserve and protect the rights of the Owner and Engineer under the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the subcontract agreement, the benefit of all rights, remedies and redress against the Contractor that the Contractor, by the Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with Sub-Subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the subcontract agreement, copies of the Contract Documents to which the Subcontractor will be bound, and, upon written request of the Subcontractor, identify to the Subcontractor terms and conditions of the proposed subcontract agreement which may be at variance with the Contract Documents. Subcontractors will similarly make copies of applicable portions of such documents available to their respective proposed Sub-

Subcontractors.

5.4 CONTINGENT ASSIGNMENT OF SUBCONTRACTS

5.4.1 Each subcontract agreement for a portion of the Work is assigned by the Contractor to the Owner provided that:

- 1** assignment is effective only after termination of the Contract by the Owner for cause pursuant to Paragraph **14.2** and only for those subcontract agreements which the Owner accepts by notifying the Subcontractor and Contractor in writing; and
- 2** assignment is subject to the prior rights of the surety, if any, obligated under bond relating to the Contract.

5.4.2 Upon such assignment, if the Work has been suspended for more than **30** days, the Subcontractor's compensation shall be equitably adjusted for increases in cost resulting from the suspension.

ARTICLE 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

6.1 OWNER'S RIGHT TO PERFORM CONSTRUCTION AND TO AWARD SEPARATE CONTRACTS

- 6.1.1** The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces, and to award separate contracts in connection with other portions of the Project or other construction or operations on the site under Conditions of the Contract identical or substantially similar to these including those portions related to insurance and waiver of subrogation. If the Contractor claims that delay or additional cost is involved because of such action by the Owner, the Contractor shall make such Claim as provided in Paragraph **4.3**.
- 6.1.2** When separate contracts are awarded for different portions of the Project or other construction or operations on the site, the term "Contractor" in the Contract Documents in each case shall mean the Contractor who executes each separate Owner-Contractor Agreement.
- 6.1.3** The Owner shall provide for coordination of the activities of the Owner's own forces and of each separate Contractor with the Work of the Contractor, who shall cooperate with them. The Contractor shall participate with other separate Contractors and the Owner in reviewing their construction schedules when directed to do so. The Contractor shall make any revisions to the construction schedule deemed necessary after a joint review and mutual agreement. The construction schedules shall then constitute the schedules to be used by the Contractor, separate Contractors and the Owner until subsequently revised.
- 6.1.4** Unless otherwise provided in the Contract Documents, when the Owner performs construction or operations related to the Project with the Owner's own forces, the Owner shall be deemed to be subject to the same obligations and to have the same rights which apply to the Contractor under the Conditions of the Contract, including, without excluding others, those stated in Article **3**, this Article **6** and Articles **10**, **11** and **12**.

6.2 MUTUAL RESPONSIBILITY

- 6.2.1** The Contractor shall afford the Owner and separate Contractors reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the Contractor's construction and operations with theirs as required by the Contract Documents.
- 6.2.2** If part of the Contractor's Work depends for proper execution or results upon construction or operations by the Owner or a separate Contractor, the Contractor shall, prior to proceeding with that portion of the Work, promptly report to the Engineer apparent discrepancies or defects in such other construction that would render it unsuitable for such proper execution and results. Failure of the Contractor so to report shall constitute an acknowledgment that the Owner's or separate Contractor's completed or partially completed construction is fit and proper to receive the Contractor's Work, except as to defects not then reasonably discoverable.
- 6.2.3** The Owner shall be reimbursed by the Contractor for costs incurred by the Owner which are payable to a separate Contractor because of delays, improperly timed activities or defective construction of the Contractor. The Owner shall be responsible to the Contractor for costs incurred by the Contractor because of delays, improperly timed activities, damage to the Work, or defective construction of a separate Contractor.
- 6.2.4** The Contractor shall promptly remedy damage wrongfully caused by the Contractor to completed or partially completed construction or to property of the Owner or separate Contractors as provided in Subparagraph **10.2.5**.
- 6.2.5** The Owner and each separate Contractor shall have the same responsibilities for cutting and patching as are described for the Contractor in Subparagraph **3.14**.

6.3 OWNER'S RIGHT TO CLEAN UP

- 6.3.1** If a dispute arises among the Contractor, separate Contractors and the Owner as to the responsibility under their respective contracts for maintaining the premises and surrounding area

free from waste materials and rubbish, the Owner may clean up and the Engineer will allocate the cost among those responsible.

ARTICLE 7 CHANGES IN THE WORK

7.1 GENERAL

- 7.1.1** Changes in the Work may be accomplished after execution of the Contract, and without invalidating the Contract, by Change Order, Construction Change Directive or order for a minor change in the Work, subject to the limitations stated in this Article 7 and elsewhere in the Contract Documents.
- 7.1.2** A Change Order shall be based upon agreement among the Owner, Contractor and Engineer; a Construction Change Directive requires agreement by the Owner and Engineer and may or may not be agreed to by the Contractor; an order for a minor change in the Work may be issued by the Engineer alone.
- 7.1.3** Changes in the Work shall be performed under applicable provisions of the Contract Documents, and the Contractor shall proceed promptly, unless otherwise provided in the Change Order, Construction Change Directive or order for a minor change in the Work.

7.2 CHANGE ORDERS

- 7.2.1** A Change Order is a written instrument prepared by the Engineer and signed by the Owner, Contractor and Engineer, stating their agreement upon all of the following:
- 1 change in the Work;
 - 2 the amount of the adjustment, if any, in the Contract Sum; and
 - 3 the extent of the adjustment, if any, in the Contract Time.
- 7.2.2** Methods used in determining adjustments to the Contract Sum may include those listed in Subparagraph 7.3.3.

7.3 CONSTRUCTION CHANGE DIRECTIVES

- 7.3.1** A Construction Change Directive is a written order prepared by the Engineer and signed by the Owner and Engineer, directing a change in the Work prior to agreement on adjustment, if any, in the Contract Sum or Contract Time, or both. The Owner may by Construction Change Directive, without invalidating the Contract, order changes in the Work within the general scope of the Contract consisting of additions, deletions or other revisions, the Contract Sum and Contract Time being adjusted accordingly.
- 7.3.2** A Construction Change Directive shall be used in the absence of total agreement on the terms of a Change Order.
- 7.3.3** If the Construction Change directive provides for an adjustment to the Contract Sum, the adjustment shall be based on one of the following methods:
- 1 mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation;
 - 2 unit prices stated in the Contract Documents or subsequently agreed upon;
 - 3 cost to be determined in a manner agreed upon by the parties and a mutually acceptable fixed or percentage fee; or
 - 4 as provided in Subparagraph 7.3.6.
- 7.3.4** Upon receipt of a Construction Change Directive, the Contractor shall promptly proceed with the change in the Work involved and advise the Engineer of the Contractor's agreement or disagreement with the method, if any, provided in the Construction Change Directive for determining the proposed adjustment in the Contract Sum or Contract Time.
- 7.3.5** A Construction Change Directive signed by the Contractor indicates the agreement of the Contractor therewith, including adjustment in Contract Sum and Contract Time or the method for determining them. Such agreement shall be effective immediately and shall be recorded as a Change Order.

7.3.6 If the Contractor does not respond promptly or disagrees with the method for adjustment in the Contract Sum, the method and the adjustment shall be determined by the Engineer on the basis of reasonable expenditures and savings of those performing the Work attributable to the change, including, in case of an increase in the Contract Sum, a reasonable allowance for overhead and profit. In such case, and also under Clause **7.3.3.3**, the Contractor shall keep and present, in such form as the Engineer may prescribe, an itemized accounting together with appropriate supporting data. Unless otherwise provided in the Contract Documents, costs for the purposes of this Subparagraph **7.3.6** shall be limited to the following:

- 1** costs of labor, including social security, old age and unemployment insurance, fringe benefits required by agreement or custom, and workers' compensation insurance;
- 2** costs of materials, supplies and equipment, including cost of transportation, whether incorporated or consumed;
- 3** rental costs of machinery and equipment, exclusive of hand tools, whether rented from the Contractor or others;
- 4** costs of premiums for all bonds and insurance, permit fees, and sales, use or similar taxes related to the Work; and
- 5** additional costs of supervision and field office personnel directly attributable to the change.

7.3.7. The amount of credit to be allowed by the Contractor to the Owner for a deletion or change which results in a net decrease in the Contract Sum shall be actual net cost as confirmed by the Engineer. When both additions and credits covering related Work or substitutions are involved in a change, the allowance for overhead and profit shall be figured on the basis of net increase, if any, with respect to that change.

7.3.8 Pending final determination of the total cost of a Construction Change Directive to the Owner, amounts not in dispute for such changes in the Work shall be included in Applications for Payment accompanied by a Change Order indicating the parties' agreement with part or all of such costs. For any portion of such cost that remains in dispute, the Engineer will make an interim determination for purposes of monthly certification for payment for those costs. That determination of cost shall adjust the Contract Sum on the same basis as a Change Order, subject to the right of either party to disagree and assert a claim in accordance with Article **4**.

7.3.9 When the Owner and Contractor agree with the determination made by the Engineer concerning the adjustments in the Contract Sum and Contract Time, or otherwise reach agreement upon the adjustments, such agreement shall be effective immediately and shall be recorded by preparation and execution of an appropriate Change Order.

7.4 MINOR CHANGES IN THE WORK

7.4.1 The Engineer will have authority to order minor changes in the Work not involving adjustment in the Contract Sum or extension of the Contract Time and not inconsistent with the intent of the Contract Documents. Such changes shall be effected by written order and shall be binding on the Owner and Contractor. The Contractor shall carry out such written orders promptly.

ARTICLE 8 TIME

8.1 DEFINITIONS

- 8.1.1** Unless otherwise provided, Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work.
- 8.1.2** The date of commencement of the Work is the date established in the Agreement. The date shall not be postponed by the failure to act of the Contractor or of persons or entities for whom the Contractor is responsible.
- 8.1.3** The date of Substantial Completion is the date certified by the Engineer in accordance with Paragraph **9.8**.
- 8.1.4** The term "day" as used in the Contract Documents shall mean calendar day unless otherwise specifically defined.

8.2 PROGRESS AND COMPLETION

- 8.2.1** Time limits stated in the Contract Documents are of the essence of the Contract. By executing the Agreement the Contractor confirms that the Contract Time is a reasonable period for performing the work.
- 8.2.2** The Contractor shall not knowingly, except by agreement or instruction of the Owner in writing, prematurely commence operations on the site or elsewhere prior to the effective date of insurance required by Article **11** to be furnished by the Contractor and Owner. The date of commencement of the Work shall not be changed by the effective date of such insurance. Unless the date of commencement is established by the Contract Documents or a notice to proceed given by the Owner, the Contractor shall notify the Owner in writing not less than five days or other agreed period before commencing the Work to permit the timely filing of mortgages, mechanic's liens and other security interests.
- 8.2.3** The Contractor shall proceed with the project expeditiously and continuously with adequate forces and shall achieve Substantial Completion within the Contract Time. Contractor shall progress with and maintain continuous construction even if construction is ahead of the approved construction schedule.

If the percentage dollar value of the completed work is 15% or more below the dollar value of work that should have been completed in accordance with the approved construction schedule, further payment under this contract to Contractor shall be suspended until the percentage dollar value of completed work is within 5% of the dollar value of work that should have been completed in accordance with the approved construction schedule.

8.3 DELAYS AND EXTENSIONS OF TIME

- 8.3.1** If the Contractor is delayed at any time in the commencement or progress of the Work by an act or neglect of the Owner or Engineer, or of an employee of either, or of a separate Contractor employed by the Owner, or by changes ordered in the Work, or by labor disputes, fire, unusual delay in deliveries; unavoidable casualties or other causes beyond the Contractor's control, then the Contract Time shall be extended by Change Order for such reasonable time as the Engineer may determine.
- 8.3.2** Claims relating to time shall be made in accordance with applicable provisions of Paragraph **4.3**.

ARTICLE 9 PAYMENTS AND COMPLETION

9.1 CONTRACT SUM

9.1.1 The Contract Sum is stated in the Agreement and, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

9.2 SCHEDULE OF VALUES

9.2.1 Before the first Application for Payment, the Contractor shall submit to the Engineer a schedule of values allocated to various portions of the Work, prepared in such form and supported by such data to substantiate its accuracy as the Engineer may require. This schedule, unless objected to by the Engineer, shall be used as a basis for reviewing the Contractor's Applications for Payment.

9.3 APPLICATIONS FOR PAYMENT

9.3.1 At least ten days before the date established for each progress payment, the Contractor shall submit to the Engineer an itemized Application for Payment for operations completed in accordance with the schedule of values. Such application shall be notarized, if required, and supported by such data substantiating the Contractor's right to payment as the Owner or Engineer may require, such as copies of requisitions from Subcontractors and material suppliers, and reflecting retainage if provided for in the Contract Documents.

9.3.1.1 As provided in Subparagraph 7.3.8, such applications may include requests for payment on account of changes in the Work which have been properly authorized by Construction Change Directives, or by interim determination of the Engineer, but not yet included in Change Orders.

9.3.1.2 Such applications may not include requests for payment for portions of the Work for which the Contractor does not intend to pay to a Subcontractor or material supplier, unless such Work has been performed by others whom the Contractor intends to pay.

9.3.2 Unless otherwise provided in the Contract Documents, payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment suitably stored off the site at a location agreed upon in writing. Payment for materials and equipment stored on or off the site shall be conditioned upon compliance by the Contractor with procedures satisfactory to the Owner to establish the Owner's title to such materials and equipment or otherwise protect the Owner's interest, and shall include the costs of applicable insurance, storage and transportation to the site for such materials and equipment stored off the site.

9.3.3 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for Payment all Work for which Certificates for Payment have been previously issued and payments received from the Owner shall, to the best of the Contractor's knowledge, information and belief, be free and clear of liens, claims, security interests or encumbrances in favor of the Contractor, Subcontractors, material suppliers, or other persons or entities making a claim by reason of having provided labor, materials and equipment relating to the Work.

9.4 CERTIFICATES FOR PAYMENT

9.4.1 The Engineer will, within seven days after receipt of the Contractor's Application for Payment, either issue to the Owner a Certificate for Payment, with a copy to the Contractor, for such amount as the Engineer determines is properly due, or notify the Contractor and Owner in writing of the Engineer's reasons for withholding certification in whole or in part as provided in Subparagraph 9.5.1.

9.4.2 The issuance of a Certificate for Payment will constitute a representation by the Engineer to the Owner, based on the Engineer's evaluation of the Work and the data comprising the Application for Payment, that the Work has progressed to the point indicated and that, to the best of the Engineer's knowledge, information and belief, the quality of the Work is in accordance with the Contract Documents. The foregoing representations are subject to an evaluation of the Work for conformance with the Contract Documents upon Substantial Completion, to results of subsequent tests and inspections, to correction of minor deviations from the Contract Documents prior to completion and to specific qualifications expressed by the Engineer. The issuance of a Certificate for Payment will further constitute a representation that the Contractor is entitled to payment in the amount certified. However, the issuance of a Certificate for Payment will not be a representation that the Engineer has (1) made exhaustive or continuous on-site inspections to check the quality or quantity of the Work, (2) reviewed construction means, methods, techniques, sequences or procedures, (3) reviewed copies of requisitions received from Subcontractors and material suppliers and other data requested by the Owner to substantiate the Contractor's right to payment, or (4) made examination to

ascertain how or for what purpose the Contractor has used money previously paid on account of the Contract Sum.

9.5 DECISIONS TO WITHHOLD CERTIFICATION

9.5.1 The Engineer may withhold a Certificate for Payment in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Engineer's opinion the representations to the Owner required by Subparagraph **9.4.2** cannot be made. If the Engineer is unable to certify payment in the amount of the Application, the Engineer will notify the Contractor and Owner as provided in Subparagraph **9.4.1**. If the Contractor and Engineer cannot agree on a revised amount, the Engineer will promptly issue a Certificate for Payment for the amount for which the Engineer is able to make such representations to the Owner. The Engineer may also withhold a Certificate for Payment or, because of subsequently discovered evidence, may nullify the whole or a part of a Certificate for Payment previously issued, to such extent as may be necessary in the Engineer's opinion to protect the Owner from loss for which the Contractor is responsible, including loss resulting from acts and omissions described in Subparagraph **3.3.2**, because of:

- 1 defective Work not remedied;
- 2 third party claims filed or reasonable evidence indicating probable filing of such claims unless security acceptable to the Owner is provided by the Contractor;
- 3 failure of the Contractor to make payments properly to Subcontractors or for labor, materials or equipment;
- 4 reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum;
- 5 damage to the Owner or another Contractor;
- 6 reasonable evidence that the Work will not be completed within the Contract Time, and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay; or
- 7 persistent failure to carry out the Work in accordance with the Contract Documents.

9.5.2 When the above reasons for withholding certification are removed, certification will be made for amounts previously withheld.

9.6 PROGRESS PAYMENTS

9.6.1 After the Engineer has issued a Certificate for Payment, the Owner shall make payment in the manner and within the time provided in the Contract Documents, and shall so notify the Engineer.

9.6.2 The Contractor shall promptly pay each Subcontractor, upon receipt of payment from the Owner, out of the amount paid to the Contractor on account of such Subcontractor's portion of the Work, the amount to which said Subcontractor is entitled, reflecting percentages actually retained from payments to the Contractor on account of such Subcontractor's portion of the Work. The Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to Sub-Subcontractors in a similar manner.

9.6.3 The Engineer will, on request, furnish to a Subcontractor, if practicable, information regarding percentages of completion or amounts applied for by the Contractor and action taken thereon by the Engineer and Owner on account of portions of the Work done by such Subcontractor.

9.6.4 Neither the Owner nor Engineer shall have an obligation to pay or to see to the payment of money to a Subcontractor except as may otherwise be required by law.

9.6.5 Payment to material suppliers shall be treated in a manner similar to that provided in Subparagraphs **9.6.2**, **9.6.3** and **9.6.4**.

9.6.6 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall not constitute acceptance of Work not in accordance with the Contract Documents.

9.6.7 Unless the Contractor provides the Owner with a payment bond in the full penal sum of the Contract Sum, payments received by the Contractor for Work properly performed by Subcontractors and suppliers shall be held by the Contractor for those Subcontractors or suppliers who performed Work or furnished materials, or both, under contract with the Contractor for which payment was made by the Owner. Nothing contained herein shall require money to be placed in a separate account and not commingled with money of the Contractor, shall create any fiduciary liability or tort liability on the part of the Contractor for breach of trust or shall entitle any person or entity to an award of punitive damages against the Contractor for breach of the requirements of this provision.

9.7 FAILURE OF PAYMENT

9.7.1 If the Engineer does not issue a Certificate for Payment, through no fault of the Contractor, within seven days after receipt of the Contractor's Application for Payment, or if the Owner does not pay the Contractor within seven days after the date established in the Contract Documents the amount certified by the Engineer or awarded by arbitration, then the Contractor may, upon seven additional days' written notice to the Owner and Engineer, stop the Work until payment of the amount owing has been received. The Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shut-down, delay and start-up, plus interest as provided for in the Contract Documents.

9.8 SUBSTANTIAL COMPLETION

9.8.1 Substantial Completion is the stage in the progress of the Work when the Work or designated portion thereof is sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work for its intended use.

9.8.2 When the Contractor considers that the Work, or a portion thereof which the Owner agrees to accept separately, is substantially complete, the Contractor shall prepare and submit to the Engineer a comprehensive list of items to be completed or corrected prior to final payment. Failure to include an item on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

9.8.3 Upon receipt of the Contractor's list, the Engineer will make an inspection to determine whether the Work or designated portion thereof is substantially complete. If the Engineer's inspection discloses any item, whether or not included on the Contractor's list, which is not sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work or designated portion thereof for its intended use, the Contractor shall, before issuance of the Certificate of Substantial Completion, complete or correct such item upon notification by the Engineer. In such case, the Contractor shall then submit a request for another inspection by the Engineer to determine Substantial Completion.

9.8.4 When the Work or designated portion thereof is substantially complete, the Engineer will prepare a Certificate of Substantial Completion which shall establish the date of Substantial Completion, shall establish responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work and insurance, and shall fix the time within which the Contractor shall finish all items on the list accompanying the Certificate, Warranties required by the Contract Documents shall commence on the date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion.

9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor for their written acceptance of responsibilities assigned to them in such Certificate. Upon such acceptance and consent of surety, if any, the Owner shall make payment of retainage applying to such Work or designated portion thereof. Such payment shall be adjusted for Work that is incomplete or not in accordance with the requirements of the Contract Documents.

9.9 PARTIAL OCCUPANCY OR USE

9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer as required under Article 11 and authorized by public authorities having jurisdiction over the Work. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage, if any, security, maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor shall prepare and submit a list to the Engineer as provided under Subparagraph 9.8.2. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner and Contractor or, if no agreement is reached, by decision of the Engineer.

9.9.2 Immediately prior to such partial occupancy or use, the Owner, Contractor and Engineer shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

9.10 FINAL COMPLETION AND FINAL PAYMENT

9.10.1 Upon receipt of written notice that the Work is ready for final inspection and acceptance and upon receipt of a

final Application for Payment, the Engineer will promptly make such inspection and, when the Engineer finds the Work acceptable under the Contract Documents and the Contract fully performed, the Engineer will promptly issue a final Certificate for Payment stating that to the best of the Engineer's knowledge, information and belief, and on the basis of the Engineer's on-site visits and inspections, the Work has been completed in accordance with terms and conditions of the Contract Documents and that the entire balance found to be due the Contractor and noted in the final Certificate is due and payable. The Engineer's final Certificate for Payment will constitute a further representation that conditions listed in Subparagraph 9.10.2 as precedent to the Contractor's being entitled to final payment have been fulfilled.

9.10.2 Neither final payment nor any remaining retained percentage shall become due until the Contractor submits to the Engineer (1) an affidavit that payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or the Owner's property might be responsible or encumbered (less amounts withheld by Owner) have been paid or otherwise satisfied, (2) a certificate evidencing that insurance required by the Contract Documents to remain in force after final payment is currently in effect and will not be canceled or allowed to expire until at least 30 days' prior written notice has been given to the Owner, (3) a written statement that the Contractor knows of no substantial reason that the insurance will not be renewable to cover the period required by the Contract Documents, (4) consent of surety, if any, to final payment and (5), if required by the Owner, other data establishing payment or satisfaction of obligations, such as receipts, releases and waivers of liens, claims, security interests or encumbrances arising out of the Contract, to the extent and in such form as may be designated by the Owner. If a Subcontractor refuses to furnish a release or waiver required by the Owner, the Contractor may furnish a bond satisfactory to the Owner to indemnify the Owner against such lien. If such lien remains unsatisfied after payments are made, the Contractor shall refund to the Owner all money that the Owner may be compelled to pay in discharging such lien, including all costs and reasonable attorneys' fees.

9.10.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by issuance of Change Orders affecting final completion, and the Engineer so confirms, the Owner shall, upon application by the Contractor and certification by the Engineer, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed and accepted. If the remaining balance for Work not fully completed or corrected is less than retainage stipulated in the Contract Documents, and if bonds have been furnished, the written consent of surety to payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Engineer prior to certification of such payment. Such payment shall be made under terms and conditions governing final payment, except that it shall not constitute a waiver of claims.

9.10.4 The making of final payment shall constitute a waiver of Claims by the Owner except those arising from:

- 1 liens, claims, security interests or encumbrances arising out of the Contract and unsettled;
- 2 failure of the Work to comply with the requirements of the Contract Documents; or
- 3 terms of special warranties required by the Contract Documents.

9.10.5 Acceptance of final payment by the Contractor, a Subcontractor or material supplier shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

10.1 SAFETY PRECAUTIONS AND PROGRAMS

10.1.1 The Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the performance of the Contract.

10.2 SAFETY OF PERSONS AND PROPERTY

10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury or loss to:

- 1 employees on the Work and other persons who may be affected thereby;
- 2 the Work and materials and equipment to be incorporated therein, whether in storage on or off the site, under care, custody or control of the Contractor or the Contractor's Subcontractors or Sub-Subcontractors; and
- 3 other property at the site or adjacent thereto, such as trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal, relocation or replacement in the course of construction.

10.2.2 The Contractor shall give notices and comply with applicable laws, ordinances, rules, regulations and lawful orders of public authorities bearing on safety of persons or property or their protection from damage, injury or loss.

10.2.3 The Contractor shall erect and maintain, as required by existing conditions and performance of the Contract, reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards, promulgating safety regulations and notifying owners and users of adjacent sites and utilities.

10.2.4 When use or storage of explosives or other hazardous materials or equipment or unusual methods are necessary for execution of the Work, the Contractor shall exercise utmost care and carry on such activities under supervision of properly qualified personnel.

10.2.5 The Contractor shall promptly remedy damage and loss (other than damage or loss insured under property insurance required by the Contract Documents) to property referred to in Clauses **10.2.1.2** and **10.2.1.3** caused in whole or in part by the Contractor, a Subcontractor, a Sub-Subcontractor, or anyone directly or indirectly employed by any of them, or by anyone for whose acts they may be liable and for which the Contractor is responsible under Clauses **10.2.1.2** and **10.2.1.3**, except damage or loss attributable to acts or omissions of the Owner or Engineer or anyone directly or indirectly employed by either of them, or by anyone for whose acts either of them may be liable, and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to the Contractor's obligations under Paragraph **3.18**.

10.2.6 The Contractor shall designate a responsible member of the Contractor's organization at the site whose duty shall be the prevention of accidents. This person shall be the Contractor's superintendent unless otherwise designated by the Contractor in writing to the Owner and Engineer.

10.2.7 The Contractor shall not load or permit any part of the construction or site to be loaded so as to endanger its safety.

10.3 EMERGENCIES

10.3.1 In an emergency affecting safety of persons or property, the Contractor shall act, at the Contractor's discretion, to prevent threatened damage, injury or loss. Additional compensation or extension of time claimed by the Contractor on account of an emergency shall be determined as provided in Paragraph **4.3** and Article **7**.

ARTICLE 11 INSURANCE AND BONDS

11.1 CONTRACTOR'S LIABILITY INSURANCE

11.1.1 The Contractor shall purchase from and maintain in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located such insurance as will protect the Contractor from claims set forth below which may arise out of or result from the Contractor's operations under the Contract and for which the Contractor may be legally liable, whether such operations be by the Contractor or by a Subcontractor or by anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable.

- 1 claims under workers' compensation, disability benefit and other similar employee benefit acts which are applicable to the Work to be performed;
- 2 claims for damages because of bodily injury, occupational sickness or disease, or death of the Contractor's employees;
- 3 claims for damages because of bodily injury, sickness or disease, or death of any person other than the Contractor's employees;
- 4 claims for damages insured by usual personal injury liability coverage;
- 5 claims for damages, other than to the Work itself, because of injury to or destruction of tangible property, including loss of use resulting therefrom;
- 6 claims for damages because of bodily injury, death of a person or property damage arising out of ownership, maintenance or use of a motor vehicle;
- 7 claims for bodily injury or property damage arising out of completed operations; and
- 8 claims involving contractual liability insurance applicable to the Contractor's obligations under Paragraph **3.18**.

11.1.2 The insurance required by Subparagraph **11.1.1** shall be written for not less than limits of liability specified in the Contract Documents or required by law, whichever coverage is greater. Coverages, whether written on an occurrence or claims-made basis, shall be maintained without interruption from date of commencement of the Work until date of final payment and termination of any coverage required to be maintained after final payment.

11.1.3 Certificates of insurance acceptable to the Owner shall be filed with the Owner prior to commencement of the Work. These certificates and the insurance policies required by this Paragraph **11.1** shall contain a provision that coverages afforded under the policies will not be canceled or allowed to expire until at least **30** days prior written notice has been given to the Owner. If any of the foregoing insurance coverages are required to remain in force after final payment and are reasonably available, an additional certificate evidencing continuation of such coverage shall be submitted with the final Application for Payment as required by Subparagraph **9.10.2**. Information concerning reduction of coverage on account of revised limits or claims paid under the General Aggregate, or both, shall be furnished by the Contractor with reasonable promptness in accordance with the Contractor's information and belief.

11.2 INDEMNIFICATION AND INSURANCE

11.2.1. Contractor agrees to save harmless, indemnify, and defend Owner and its, agents, officers and employees from any and all claims, losses, penalties, interest, demands, judgments, and costs of suit, including attorneys fees and paralegals' fees, for any expense, damage or liability incurred by any of them, whether for personal injury, death, property damage, direct or consequential damages, or economic loss, including environmental impairment, arising directly or indirectly on account of or in connection with the work done by Contractor under this agreement or by any person, firm or corporation (including but not limited to the Engineer/engineer) to whom any portion of the work is subcontracted by Contractor or resulting from the use by Contractor, or by any one for whom Contractor is legally liable, of any materials, tools, machinery or other property of Owner. Owner and Contractor agree the first \$100.00 of the contract amount paid by Owner to Contractor shall be given as separate consideration for this indemnification, and any other indemnification of Owner by Contractor provided for within the Contract Documents, the sufficiency of such separate consideration being acknowledged by Contractor by Contractor's acceptance and execution of the agreement. The Contractor's obligation shall not be limited by, or in any way to, any insurance coverage or by any provision in or exclusion or omission from any policy of insurance. The Contractor agrees to pay on behalf of Santa Rosa County, as well as provide a legal defense for the Owner, both of which will be done only if and when requested by the Owner, for all claims made. Such payment on the behalf of the Owner shall be in addition to any and all other legal remedies available to the Owner and shall not be considered to be the

Owner's exclusive remedy.

- 11.2.2.** Contractor shall obtain and carry, at all times during its performance under the Contract Documents, insurance of the types and in the amounts set forth in Article 11. All insurance policies shall be from responsible companies duly authorized to do business in the State of Florida and/or responsible risk retention group insurance companies or trusts which are registered with the State of Florida. Foreign or offshore insurance carriers are not acceptable for work under this contract unless admitted to the State of Florida. All commercial insurance carriers providing the Contractor with required insurance shall be "A" (excellent) rated with a minimum financial size category of "IX", according to the A. M. Best Key Rating Guide, latest edition. Within ten (10) calendar days after notice of award is received by Contractor and prior to the commencement of work, Contractor shall provide Owner with properly executed certificates of insurance to evidence Contractor's compliance with the insurance requirements of the Contract Documents. Said certificates of insurance shall be on forms approved by Owner, such as "Acord Form 25". The certificates of insurance shall be personally, manually signed by the authorized representatives of the insurance company/companies shown on the certificates of insurance, with proof that they are authorized representatives thereof. Certificates of insurance shall be mailed to Santa Rosa County Board of County Commissioners in care of: Anthony Gomillion, County Administrator, 6495 Caroline Street, Suite D, Milton, Florida 32570. In addition, true and exact copies of all insurance policies required hereunder shall be provided to Owner, on a timely basis, when requested by Owner.
- 11.2.3.** The certificates of insurance and required insurance policies shall contain provisions that thirty (30) days prior written notice by registered or certified mail shall be given Owner of any cancellation, intent not to renew, or reduction in the policies or coverages, except in the application of the aggregate limits provisions. In the event of a reduction in the aggregate limit of any policy, Contractor shall immediately take steps to have the aggregate limit reinstated to the full extent permitted under such policy.
- 11.2.4.** All insurance coverages of the Contractor shall be primary to any insurance or self insurance program carried by the Owner applicable to this project. The acceptance by Owner of any certificate of insurance does not constitute approval or agreement by the Owner that the insurance requirements have been satisfied or that the insurance policy shown on the certificate of insurance is in compliance with the requirements of the Contract Documents. No work shall commence at the project site unless and until the required certificates of insurance are received by the Owner
- 11.2.5.** Contractor shall require each of its Subcontractors to procure and maintain, until the completion of the Subcontractor's work, insurance of the types and to the limits specified in Article 11, unless such insurance requirements for the Subcontractor is expressly waived in writing by the Owner. All liability insurance policies, other than professional liability, worker's compensation and employer's liability policies, obtained by Contractor to meet the requirements of the Contract Documents shall name the Santa Rosa County Board of County Commissioners as an additional insured and shall contain severability of interest provisions. The Board of County Commissioners shall also be designated as certificate holder with the address of 6495 Caroline Street, Suite M, Milton, Florida 32570. If any insurance provided pursuant to the Contract Documents expires prior to the completion of the work, renewal certificates of insurance and, if requested by Owner, certified, true copies of the renewal policies, shall be furnished by Contractor within thirty (30) days prior to the date of expiration. Upon expiration of an insurance policy term during the course of work under the contract, succeeding insurance policies shall be consecutive to the expiring policy.
- 11.2.6** All liability policies shall be underwritten on the "occurrence" basis, unless otherwise approved in writing by the county division of risk management. "Claims made" policies, if approved by the risk manager, and subsequent insurance certificates shall provide a "retro-date" which shall include the effective date of the contract. "Claims-made" renewals or carrier and policy replacements shall reflect the original "retro-date."
- 11.2.7** Should at any time the Contractor not maintain the insurance coverages required herein, the Owner may terminate the agreement or at its sole discretion shall be authorized to purchase such coverages and charge the Contractor for such coverages purchased. The Owner shall be under no obligation to purchase such insurance, nor shall it be responsible for the coverages purchased or the insurance company or companies used. The decision of the Owner to purchase such insurance coverages shall in no way be construed to be a waiver of any of its rights under the Contract Documents.
- 11.2.8** Contractor shall submit to Owner a copy of all accident reports arising out of any personal injuries or property damages arising or alleged to have arisen on account of any work by Contractor or Subcontractor under the Contract

Documents.

11.2.9 Duty to Provide Legal Defense. The Contractor agrees to pay, to Santa Rosa County, as well as provide a legal defense for the Owner, which shall include attorneys' fees and costs, both of which will be done only if and when requested by the Owner, for all claims as described in paragraph **13.1**. Such payment on the behalf of the Owner shall be in addition to any and all other legal remedies available to the Owner and shall not be considered to be the Owner's exclusive remedy.

11.3 PERFORMANCE BOND AND PAYMENT BOND

11.3.1 BONDS.

11.3.1.1 Contractor shall provide performance and payment bonds, in the form prescribed in Exhibit B, in the amount of 100% of the contract amount, the costs of which to be paid by Contractor. The performance and payment bonds shall be underwritten by a surety authorized to do business in the State of Florida and otherwise acceptable to Owner; provided; however, the surety shall be rated as "A" or better and Class XII or higher rating as to financial size category and the amount required shall not exceed 2% of the reported policy holders surplus, all as reported in the most current best key rating guide, published by A.M. Best Company, Inc. of 75 Fulton Street, New York, New York 10038.

11.3.1.2 If the surety for any bond furnished by Contractor is declared bankrupt, becomes insolvent, its right to do business is terminated in the State of Florida, or it ceases to meet the requirements imposed by the Contract Document, the Contractor shall, within five (5) calendar days thereafter, substitute another bond and surety, both of which shall be subject to the Owner's approval.

11.3.1.3 As per Florida Statutes, Section 255.05, the Contractor shall be required to execute and record the performance and payment bonds. The bonds must state the name and principal business address of both the principal and the surety and a description of the project sufficient to identify it.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

12.1 UNCOVERING OF WORK

12.1.1 If a portion of the Work is covered contrary to the Engineer's request or to requirements specifically expressed in the Contract Documents, it must, if required in writing by the Engineer, be uncovered for the Engineer's examination and be replaced at the Contractor's expense without change in the Contract Time.

12.1.2 If a portion of the Work has been covered which the Engineer has not specifically requested to examine prior to its being covered, the Engineer may request to see such Work and it shall be uncovered by the Contractor. If such Work is in accordance with the Contract Documents, costs of uncovering and replacement shall, by appropriate Change Order, be at the Owner's expense. If such Work is not in accordance with the Contract Documents, correction shall be at the Contractor's expense unless the condition was caused by the Owner or a separate Contractor in which event the Owner shall be responsible for payment of such costs.

12.2 CORRECTION OF WORK

12.2.1 BEFORE OR AFTER SUBSTANTIAL COMPLETION

12.2.1.1 The Contractor shall promptly correct Work rejected by the Engineer or failing to conform to the requirements of the Contract Documents, whether discovered before or after Substantial Completion and whether or not fabricated, installed or completed. Costs of correcting such rejected Work, including additional testing and inspections and compensation for the Engineer's services and expenses made necessary thereby, shall be at the Contractor's expense.

12.2.2 AFTER SUBSTANTIAL COMPLETION

12.2.2.1 In addition to the Contractor's obligations under Paragraph **3.5**, if, within one year after the date of Substantial Completion of the Work or designated portion thereof or after the date for commencement of warranties established under Subparagraph **9.9.1**, or by terms of an applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the Owner to do so unless the Owner has previously given the Contractor a written acceptance of such condition. The Owner shall give such notice promptly after discovery of the condition. During the one- year period for correction of Work, if the Owner fails to notify the Contractor and give the Contractor an opportunity to make the correction, the Owner waives the rights to require correction by the Contractor and to make a claim for breach of warranty. If the Contractor fails to correct nonconforming Work within a reasonable time during that period after receipt of

notice from the Owner or Engineer, the Owner may correct it in accordance with Paragraph 2.4.

12.2.2.2 The one-year period for correction of Work shall be extended with respect to portions of Work first performed after Substantial Completion by the period of time between Substantial Completion and the actual performance of the Work.

12.2.2.3 The one-year period for correction of Work shall not be extended by corrective Work performed by the Contractor pursuant to this Paragraph 12.2.

12.2.3 The Contractor shall remove from the site portions of the Work which are not in accordance with the requirements of the Contract Documents and are neither corrected by the Contractor nor accepted by the Owner.

12.2.4 The Contractor shall bear the cost of correcting destroyed or damaged construction, whether completed or partially completed, of the Owner or separate Contractors caused by the Contractor's correction or removal of Work which is not in accordance with the requirements of the Contract Documents.

12.2.5 Nothing contained in this Paragraph 12.2 shall be construed to establish a period of limitation with respect to other obligations which the Contractor might have under the Contract Documents. Establishment of the one-year period for correction of Work as described in Subparagraph 12.2.2 relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to the Contractor's obligations other than specifically to correct the Work.

12.3 ACCEPTANCE OF NONCONFORMING WORK

12.3.1 If the Owner prefers to accept Work which is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Sum will be reduced as appropriate and equitable. Such adjustment shall be effected whether or not final payment has been made.

ARTICLE 13 MISCELLANEOUS PROVISIONS

13.1 GOVERNING LAW

13.1.1 The Contract shall be governed by the law of the place where the Project is located.

13.2 SUCCESSORS AND ASSIGNS

13.2.1 The Owner and Contractor respectively bind themselves, their partners, successors, assigns and legal representatives to the other party hereto and to partners, successors, assigns and legal representatives of such other party in respect to covenants, agreements and obligations contained in the Contract Documents. Except as provided in Subparagraph 13.2.2, neither party to the Contract shall assign the Contract as a whole without written consent of the other. If either party attempts to make such an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations under the Contract.

13.2.2 The Owner may, without consent of the Contractor, assign the Contract to an institutional lender providing construction financing for the Project. In such event, the lender shall assume the Owner's rights and obligations under the Contract Documents. The Contractor shall execute all consents reasonably required to facilitate such assignment.

13.3 WRITTEN NOTICE

13.3.1 Written notice shall be deemed to have been duly served if delivered in person to the individual or a member of the firm or entity or to an officer of the corporation for which it was intended, or if delivered at or sent by registered or certified mail to the last business address known to the party giving notice.

13.4 RIGHTS AND REMEDIES

13.4.1 Duties and obligations imposed by the Contract Documents and rights and remedies available thereunder shall be in addition to and not a limitation of duties, obligations, rights and remedies otherwise imposed or available by law.

13.4.2 No action or failure to act by the Owner, Engineer or Contractor shall constitute a waiver of a right or duty afforded them under the Contract, nor shall such action or failure to act constitute approval of or acquiescence in a breach thereunder, except as may be specifically agreed in writing.

13.5 TESTS AND INSPECTIONS

13.5.1 Tests, inspections and approvals of portions of the Work required by the Contract Documents or by laws, ordinances, rules, regulations or orders of public authorities having jurisdiction shall be made at an appropriate time. Unless otherwise provided, the Contractor shall make arrangements for such tests, inspections and approvals with an independent testing laboratory or entity acceptable to the Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections and approvals. The Contractor shall give the Engineer timely notice of when and where tests and inspections are to be made so that the Engineer may be present for such procedures. The Owner shall bear costs of tests, inspections or approvals which do not become requirements until after bids are received or negotiations concluded.

13.5.2 If the Engineer, Owner or public authorities having jurisdiction determine that portions of the Work require additional testing, inspection or approval not included under Subparagraph 13.5.1, the Engineer will, upon written authorization from the Owner, instruct the Contractor to make arrangements for such additional testing, inspection or approval by an entity acceptable to the Owner, and the Contractor shall give timely notice to the Engineer of when and where tests and inspections are to be made so that the Engineer may be present for such procedures. Such costs, except as provided in Subparagraph 13.5.3, shall be at the Owner's expense.

13.5.3 If such procedures for testing, inspection or approval under Subparagraphs 13.5.1 and 13.5.2 reveal failure of the portions of the Work to comply with requirements established by the Contract Documents, all costs made necessary by such failure including those of repeated procedures and compensation for the Engineer's services and expenses shall be at the Contractor's expense.

13.5.4 Required certificates of testing, inspection or approval shall, unless otherwise required by the Contract Documents, be secured by the Contractor and promptly delivered to the Engineer.

13.5.5 If the Engineer is to observe tests, inspections or approvals required by the Contract Documents, the Engineer will do so promptly and, where practicable, at the normal place of testing.

13.5.6 Tests or inspections conducted pursuant to the Contract Documents shall be made promptly to avoid unreasonable delay in the Work.

13.6 INTEREST

13.6.1 Payments due and unpaid under the Contract Documents shall bear interest from the date payment is due at such rate as the parties may agree upon in writing or, in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

13.7 COMMENCEMENT OF STATUTORY LIMITATION PERIOD

13.7.1 As between the Owner and Contractor:

- 1** Before Substantial Completion. As to acts or failures to act occurring prior to the relevant date of Substantial Completion, any applicable statute of limitations shall commence to run and any alleged cause of action shall be deemed to have accrued in any and all events not later than such date of Substantial Completion;
- 2** Between Substantial Completion and Final Certificate for Payment. As to acts or failures to act occurring subsequent to the relevant date of Substantial Completion and prior to issuance of the final Certificate for Payment, any applicable statute of limitations shall commence to run and any alleged cause of action shall be deemed to have accrued in any and all events not later than the date of issuance of the final Certificate for Payment; and
- 3** After Final Certificate for Payment. As to acts or failures to act occurring after the relevant date of issuance of the final Certificate for Payment, any applicable statute of limitations shall commence to run and any alleged cause of action shall be deemed to have accrued in any and all events not later than the date of any act or failure to act by the Contractor pursuant to any Warranty provided under Paragraph **3.5**, the date of any correction of the Work or failure to correct the Work by the Contractor under Paragraph **12.2**, or the date of actual commission of any other act or failure to perform any duty or obligation by the Contractor or Owner, whichever occurs last.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

14.1 TERMINATION BY THE CONTRACTOR

14.1.1 The Contractor may terminate the Contract if the Work is stopped for a period of **30** consecutive days through no act or fault of the Contractor or a Subcontractor, Sub-Subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, for any of the following reasons.

- 1** issuance of an order of a court or other public authority having jurisdiction which requires all Work to be stopped;
- 2** an act of government, such as a declaration of national emergency which requires all Work to be stopped;
- 3** because the Engineer has not issued a Certificate for Payment and has not notified the Contractor of the reason for withholding certification as provided in Subparagraph **9.4.1**, or because the Owner has not made payment on a Certificate for Payment within the time stated in the Contract Documents; or
- 4** the Owner has failed to furnish to the Contractor promptly, upon the Contractor's request, reasonable evidence as required by Subparagraph **2.2.1**.

14.1.2 The Contractor may terminate the Contract if, through no act or fault of the Contractor or a Subcontractor, Sub-Subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, repeated suspensions, delays or interruptions of the entire Work by the Owner as described in Paragraph **14.3** constitute in the aggregate more than 100 percent of the total number of days scheduled for completion, or **120** days in any 365-day period, whichever is less.

14.1.3 If one of the reasons described in Subparagraph **14.1.1** or **14.1.2** exists, the Contractor may, upon seven days' written notice to the Owner and Engineer, terminate the Contract and recover from the Owner only as provided in Subparagraph **14.3.1**.

14.1.4 *If the Work is stopped for a period of 60 consecutive days through no act or fault of the Contractor or a Subcontractor or their agents or employees or any other persons performing portions of the Work under contract with the Contractor because the Owner has persistently failed to fulfill the Owner's obligations under the Contract Documents with respect to matters important to the progress of the Work, the Contractor may, upon seven additional days' written notice to the Owner and the Engineer, terminate the Contract and recover from the Owner only as provided in Subparagraph **14.3.1**.*

14.2 TERMINATION FOR DEFAULT.

14.2.1 Contractor shall be considered in material default of the agreement and such default shall be considered cause for Owner to terminate the agreement, in whole or in part, as further set forth in this section, if Contractor: (1) fails to begin the work under the Contract Documents within the time specified herein; or (2) fails to properly and timely perform the work as directed by the Owner or as provided for in the approved progress schedule; or (3) performs the work unsuitably or neglects or refuses to remove materials or to correct or replace such work as may be rejected as unacceptable or unsuitable; or (4) discontinues the prosecution of the work; or (5) fails to resume work which has been suspended within a reasonable time after being notified to do so; or (6) becomes insolvent or is declared bankrupt, or commits any act of bankruptcy; or (7) allows any final judgment to stand against it unsatisfied for more than ten (10) days; or (8) makes an assignment for the benefit of creditors; or (9) fails to obey any applicable codes, laws, ordinances, rules or regulations with respect to the work; or (10) materially breaches any other provision of the Contract Documents.

14.2.2 Owner shall notify Contractor in writing of Contractor's default(s). If Owner determines that Contractor has not remedied and cured the default(s) within seven (7) calendar days following receipt by Contractor of said written notice, then Owner, at its option, without releasing or waiving its rights and remedies against the Contractor's sureties and without prejudice to any other right or remedy it may be entitled to hereunder or by law, may terminate Contractor's right to proceed under the agreement, in whole or in part, and take possession of all or any portion of the work and any materials, tools, equipment, and appliances of Contractor, take assignments of any of Contractor's subcontracts and purchase orders, and complete all or any portion of Contractor's work by whatever means, method or agency which Owner, in its sole discretion, may choose.

14.2.3 If Owner deems any of the foregoing remedies necessary, Contractor agrees that is shall not be entitled to receive any further payments hereunder until after the project is completed. All monies expended and all of the costs, losses, damages and extra expenses, including all management, administrative and other overhead and other direct

and indirect expenses (including attorneys' fees) or damages incurred by Owner incident to such completion, shall be deducted from the contract amount, and if such expenditures exceed the unpaid balance of the contract amount, Contractor agrees to pay promptly to Owner on demand the full amount of such excess, including costs of collection, attorney's fees (including appeals) and interest thereon at the maximum legal rate of interest until paid. If the unpaid balance of the contract amount exceeds all such costs, expenditures and damages incurred by the Owner to complete the work, such excess shall be paid to the Contractor. The amount to be paid to the Contractor or Owner, as the case may be, and this obligation for payment shall survive termination of the agreement.

14.2.4. The liability of Contractor hereunder shall extend to and include the full amount of any and all sums paid, expenses and losses incurred, damages sustained, and obligations assumed by Owner in good faith under the belief that such payments or assumptions were necessary or required, in completing the work and providing labor, materials, equipment, supplies, and other items therefor or re-letting the work, in settlement, discharge or compromise of any claims, demands, suits, and judgments pertaining to or arising out of the work hereunder.

14.2.5 If, after notice of termination of Contractor's right to proceed pursuant to this section, it is determined for any reason that Contractor was not in default, or that its default was excusable, or that Owner is not entitled to the remedies against Contractor provided herein, then Contractor's remedies against Owner shall be the same as and limited to those afforded Contractor below under subsection **14.3.1**, termination for convenience.

14.3 TERMINATION FOR CONVENIENCE AND RIGHT OF SUSPENSION.

14.3.1. Owner shall have the right to terminate this agreement without cause upon seven (7) calendar days written notice to Contractor. In the event of such termination for convenience, Contractor's recovery against Owner shall be limited to that portion of the contract amount earned through the date of termination, together with any retainage withheld and reasonable termination expenses incurred, but Contractor shall not be entitled to any other or further recovery against Owner, including, but not limited to, damages or any anticipated profit on portions of the work not performed.

14.3.2. Owner shall have the right to suspend all or any portions of the work upon giving Contractor two (2) calendar days' prior written notice of such suspension. If all or any portion of the work is so suspended, Contractor's sole and exclusive remedy shall be to seek an extension of time to its schedule in accordance with the procedures set forth in the Contract Documents. In no event shall the Contractor be entitled to any additional compensation or damages. Provided, however, if the ordered suspension exceeds three (3) months, the Contractor shall have the right to terminate the agreement with respect to that portion of the work which is subject to the ordered suspension.

SWORN STATEMENT UNDER SECTION 287.133 (3) (A),
FLORIDA STATUTES, ON PUBLIC ENTITY CRIMES
THIS FORM MUST BE SIGNED IN THE PRESENCE OF A NOTARY PUBLIC OR OTHER OFFICER
AUTHORIZED TO ADMINISTER OATHS.

1. This sworn statement is submitted to

_____ by
(print individual's name and title)
_____ for
(print name of entity submitting sworn statement)
_____ whose
business address is

_____ and (if
applicable) its Federal Employer Identification Number (FEIN)
is _____.

If the entity has no FEIN, include the Social Security Number of the individual signing this Sworn Statement:

2. I understand that a "public entity crime" as defined in Paragraph 287.133(1)(g), Florida Statutes, means a violation of any state or federal law by a person with respect to and directly related to the transaction of business with any public entity or with an agency or political subdivision of any other state or with the United States, including, but not limited to, any bid or contract for goods or services to be provided to any public entity or an agency or political subdivision of any other state or of the United States and involving antitrust, fraud, theft, bribery, collusion, racketeering, conspiracy, or material misrepresentation.

3. I understand that "convicted" or "conviction" as defined in Paragraph 287.133(1)(b), Florida Statutes, means a finding of guilt or a conviction of a public entity crime, with or without an adjudication of guilt, in any federal or state trial court of record relating to charges brought by indictment or information after July 1, 1989, as a result of a jury verdict, nonjury trial, or entry of a plea of guilty or nolo contendere.

4. I understand that an "affiliate" as defined in Paragraph 287.133(1)(a), Florida Statutes, means:

1. A predecessor or successor of a person convicted of a public entity crime; or
2. An entity under the control of any natural person who is active in the management of the entity and who has been convicted of a public entity crime. The term "affiliate" includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in the management of an affiliate. The ownership by one person of shares constituting a controlling interest in another person, or a pooling of equipment or income among persons when not for fair market value under an arm's length agreement, shall be a prima facie case that one person controls another person. A person who knowingly enters into a joint venture with a person who has been convicted of public entity crime.

5. I understand that a "person" as defined in Paragraph 287.133(1)(e), Florida Statutes, means any natural person or entity organized under the laws of any state or of the United States with legal power to enter into a binding contract and which bids or appeals to bid on contracts for the provision of goods and services let by a public entity, or which otherwise transacts or applies to transact business with a public entity. The term "person" includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in management of an entity.

6. Based on information and belief, the statement which I have marked below is true in relation to the entity submitting this sworn statement. (Indicate which statement applies.)

Neither the entity submitting this sworn statement, nor one or more of the officers, directors, executives, partners, shareholders, employees, members, or agents who are active in management of the entity, nor any affiliate of the entity have been charged with and convicted of a public entity crime subsequent to July 1, 1989.

The entity submitting this sworn statement, or one or more of the officers, directors, executives, partners, shareholders, employees, members, or agents who are active in management of the entity, or an affiliate of the entity has been charged with and convicted of a public entity crime subsequent to July 1, 1989.

The entity submitting this sworn statement, or one or more of the officers, directors, executives, partners, shareholders, employees, members, or agents who are active in management of the entity, or an affiliate of the entity has been charged with and convicted of a public entity crime subsequent to July 1, 1989. However, there has been a subsequent proceeding before a Hearing Officer of the State of Florida, Division of Administrative Hearings and the Final Order entered by the Hearing Officers determined that it was not in the public interest to place the entity submitting this sworn statement on the convicted vendor list. (ATTACH A COPY OF THE FINAL ORDER.)

I UNDERSTAND THAT THE SUBMISSION OF THIS FORM TO THE CONTRACTING OFFICER FOR THE PUBLIC ENTITY IDENTIFIED IN PARAGRAPH 1 (ONE) ABOVE IS FOR THAT PUBLIC ENTITY ONLY AND THAT THIS FORM IS VALID THROUGH DECEMBER 31 OF THE CALENDAR YEAR IN WHICH IT IS FILED. I ALSO UNDERSTAND THAT I AM REQUIRED TO INFORM THE PUBLIC ENTITY PRIOR TO ENTERING INTO A CONTRACT IN EXCESS OF THE THRESHOLD AMOUNT PROVIDED IN SECTION 287.017, FLORIDA STATUTES FOR CATEGORY TWO OF ANY CHANGE IN THE INFORMATION CONTAINED IN THIS FORM.

_____ (Signature)

Sworn to and subscribed before me this _____ day of _____, 20 .

Personally known _____

or Produced identification _____ Notary Public – State of _____

_____ My commission expires _____

(Type of identification)

_____ (Printed, typed, or stamped commissioned name of notary public.)



SANTA ROSA COUNTY PROCUREMENT DEPARTMENT

DAVID KING
Procurement Officer
davidk@santarosa.fl.gov

6495 Caroline Street, Suite J | Milton, Florida 32570

TO: Plan-holders
FROM: Dave King
Procurement Officer
DATE: October 4, 2016
REF: ADDENDUM #1 to RFP #16-061 Ortega Street Sidewalks

PROJECT ADDENDUM #1

This addendum is issued for the purpose of modifying and/or clarifying the original plans and specifications and is to be construed as being therein.

DRAWINGS:

Item 1: SIDEWALK DETAIL

Replace 5 Foot Wide Sidewalk Detail (page 7) in full

SPECIFICATIONS:

The following additions/clarifications are to be incorporated into the project scope of work

- Question: Is sod required for site restoration? If so, what kind?
Answer: Sod restoration along the right-of-way is required at all residential and business lots that have a structure. The remaining right-of-way at vacant lots shall be restored using seed and hay. The sod for the restoration shall match the adjacent home/business owners grass. If the owner has St. Augustine, use St. Augustine. If the owner has Centipede grass, use Centipede etc.
- Question: The sidewalk cross section/detail in the bid documents specifies density test for subgrade. Are density tests required?
Answer: No. Soil density tests are not required for this project. However, the contractor shall ensure the subgrade is compacted using mechanical means such as a vibratory plate tamp. (See attached amended cross section detail)
- Question: The sidewalk cross section/detail in the bid documents specifies Baha sod for restoration. Is this the only sod we can use?
Answer: Disregard the Baha note and use sod matching home/business owners adjacent sod. (See attached amended detail)
- Question: Are concrete cylinder tests required?
Answer: No. There is no concrete testing required in this project.
- Question: Is there a lay down area for the contractor to use during construction?
Answer: There are a few small areas that may be used for equipment and material storage. The county ride-of-way along the vacant properties on the east ends of



SANTA ROSA COUNTY PROCUREMENT DEPARTMENT

DAVID KING
Procurement Officer
davidk@santarosa.fl.gov

6495 Caroline Street, Suite J | Milton, Florida 32570

Laredo, El Paseo, Oliveria and Estrada Streets. Some of these locations will be suitable for equipment parking and stock piles. There is also a lay down space in the R/W at the south east end of Ortega Street. If the right-of-way laydown areas are deemed insufficient by the contractor, he/she are welcome to pursue an independent agreement with a private property owner. (There are numerous vacant lots in the project area)

- Question: The specifications require a 6" thick cross section for driveways. Does this mean remove the existing section of driveways to install a 6" thick walk through the driveway?
- Answer: No. Use existing driveways and pour/place the concrete sidewalk to the existing driveway.

- Question: Who is responsible for utility locates?
- Answer: It is the contractors responsibility to call for utility locates.

- Question: How far off the edge of pavement shall the sidewalk be constructed?
- Answer: Generally 18-24" however, this will vary along the right-of-way due to utility, mailbox and irrigation system conflicts. The sidewalk alignment shall be coordinated with the county representative prior to construction.

- Question: Who is responsible for repairing/relocating irrigation lines?
- Answer: It shall be the contractors responsibility to make any needed repairs or relocations.

- Question: Who is responsible for mailbox conflicts/relocations?
- Answer: It shall be the contractors responsibility to relocate any post type mailboxes that might be moved for sidewalk alignment. There will be no brick mailbox relocations.


This Addendum is furnished to all known prospective Proposers. Please sign and include one copy of this Addendum, with original signature, with your proposal as an acknowledgement of your having received same. You may photocopy for your records.

Sincerely,

Dave King
Procurement Officer

SIGNED: _____
COMPANY: _____

End of ADDENDUM #1

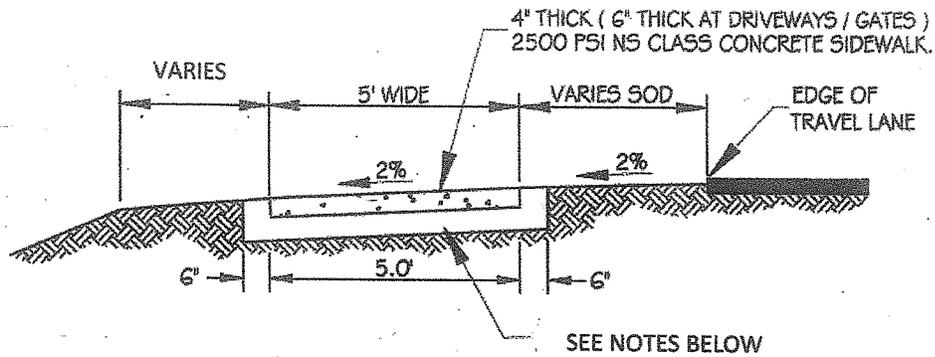

5 FOOT WIDE SIDEWALK DETAIL
N.T.S.

NOTES:

- 1) After removing vegetation and top soil, compact existing soil for base materials. Remove unsuitable soils, replace with granular fill, and compact. Santa Rosa County shall provide and deliver suitable fill as required. Fill material shall be placed and compacted by the contractor.
- 2) The sidewalk shall be constructed to match the existing grades. The sidewalk will have a transverse slope either toward or away from the road to maintain existing drainage patterns.
- 3) Sidewalks shall conform to ADA requirements.
